

File No. 04-1000-20-2016-233

July 28, 2016

s.22(1)

Dear s.22(1)

Re: Request for Access to Records under the Freedom of Information and Protection of Privacy Act (the "Act")

I am responding to your request of July 4, 2016 for:

Storm and Sewer Service records for 450 E 47th Ave Vancouver (other possible address is 451 E 48th Ave, 400 Block of E 48th Ave) for the private and city property regarding this property. I would like the records of all work completed including but not limited to camera scope, root cutting, auguring, drain cleaning. Reference number is 7849460.

Superintendent of the Sewer Department, Tony Shaw, is aware of this request.

All responsive records are attached.

Under section 52 of the Act you may ask the Information & Privacy Commissioner to review any matter related to the City's response to your request. The Act allows you 30 business days from the date you receive this notice to request a review by writing to: Office of the Information & Privacy Commissioner, info@oipc.bc.ca or by phoning 250-387-5629.

If you request a review, please provide the Commissioner's office with: 1) the request number assigned to your request (#04-1000-20-2016-233); 2) a copy of this letter; 3) a copy of your original request for information sent to the City of Vancouver; and 4) detailed reasons or grounds on which you are seeking the review.

Please do not hesitate to contact the Freedom of Information Office at foi@vancouver.ca if you have any questions.

Yours truly,

Cobi Falconer, FOI Case Manager, for
Barbara Van Fraassen

A handwritten signature in black ink, appearing to read "Cobi Falconer". The signature is fluid and cursive, with a large, sweeping flourish at the end.

Barbara J. Van Fraassen, BA
Director, Access to Information
City Clerk's Department, City of Vancouver
Email: Barbara.vanfraassen@vancouver.ca
Telephone: 604.873.7999

Encl.

:jb

Work Slip

1376
COMPLETED

SAP Charge #	Address & Location: 400 - 499 E 48TH AV					Responsible
EES751063	(CCTV 250 Comb main East to end of run for condition. Also look for connection installed 1990 to property on n/side of street address indicated as 474 E 47th but located at 481 E 48th(also cctv this connection) just east of m/h#401780. for further information;					Sewer Operations
Work Order #	Work Order Activity					Created Date
751063	Maintenance(400 E 48 CCTV Main) s.22(1)					Jun 06, 2016
Group Project #	Problem	Sub Activity	Assigned To	Crew ID		
		SCCTV	ANTHONY SHAW	S_Crew23		
Work Order Comments:						
Reference #1	WGS 751017					Billable?
Reference #2						N
Service Request #:	SR 968810					
Contact Name			Contact Phone	Contact Type		
Asset Type	Asset ID #	B.U.N	Status	Asset Area	Map # (Facet)	District
Main (C)	401780		IN_SERVICE	CBD08	Q21	5
Asset Details: C 250 Millimeter VC 60.66 Meters 4.81% [60.66 - 250 C VC 4.81% 1930]:						
Safety & Asset Notes:						
PM Schedule	Last Completed Work Order					
Crew Comments						
Found Heavy Roots 2.4m East of Downstream M.H. Need a Sucker Track to Root cut main W/O EES753149 emailed to Dispatch <div style="text-align: right;"></div>						
Work Completed Date:			Print Name:		Crew ID:	

INFOR HANSEN 8

2016/06/06 08:50

Asset



*2.4m from
downstream
MH Heavy Roots*

Current:	Layers Legend
Tool :	<input checked="" type="checkbox"/> Sew Manho
zoomin	<input type="checkbox"/> Sew Catchb
Zoom	<input type="checkbox"/> Sew Fitting
Level : 8	<input type="checkbox"/>
of 9	
0	
Scale 1 :	
1061147	
Contents	<input type="checkbox"/>

Work Slip

COMPLETED

SAP Charge #	Address & Location: 400 - 499 E 48TH AV (from EES751063 CCTV inspection found heavy roots 2.4m east of downstream m/h needs to be root cut (250 Comb))			Responsible		
EES753149				Sewer Operations		
Work Order #	Work Order Activity			Created Date		
753149	Maintenance(400 E 48 RC main)			Jun 11, 2016		
Group Project #	Problem	Sub Activity	Assigned To	Crew ID		
		SROOTCUT	ALBANO LUIS	28		
Work Order Comments:						
Reference #1				Billable?		
Reference #2				N		
Service Request #:						
Contact Name		Contact Phone	Contact Type			
Asset Type	Asset ID #	B.U.N	Status	Asset Area	Map # (Facet)	District
Main (C)	401780		IN_SERVICE	CBD08	Q21	5
Asset Details: C 250 Millimeter VC 60.66 Meters 4.81% [60.66 - 250 C VC 4.81% 1930]:						
Safety & Asset Notes:						
PM Schedule	Last Completed Work Order					
	Jun 07, 2016; 751063; Maintenance (400 E 48 CCTV Main)					
Crew Comments						
<p>Root cut Main 250 comb 60.66m. All ok!</p> <p style="text-align: right;">Job Completed </p>						
Work Completed Date:	JUNE 15, 16	Print Name:	PIERRE / KEN	Crew ID:	28	

CLEANING REPORT

Date: June 17, 16

D

C1314 C1315 B1317 B1371 B1330 1333 1336 1337 1338 1339 1347 Rental - Page:

RECORD NO: & WORK ORDER NO:	BLOCK Or ADDRESS	LOCATION				PIPE DIAMETER & FACILITY	LENGTH CLEANED	TASK & REMEDY	Complete Y/N	Schedule Next 5 Yrs or	FINDINGS & NOTES Please Circle
		MAIN ST / AVE	At or To: CROSS ST	From: MH No:	To MH No:						
EB5756043	400	E 48 th	Prince Edward to ST GEORGE	76.19	78.95	250	74.4	Root cut	Y		Clear <u>Roots</u> Solids Grease Debris MAP # <u>Q21</u> Structural Defect Poor Hydraulics Unknown CB Pumped: _____ CB Checked: _____
EB5756045	400	E 48 th	ST GEORGE	78.95	82.7	250	60.7		Y		Clear <u>Roots</u> Solids Grease Debris MAP # <u>Q21</u> Structural Defect Poor Hydraulics Unknown CB Pumped: _____ CB Checked: _____
											Clear Roots Solids Grease Debris MAP # _____ Structural Defect Poor Hydraulics Unknown CB Pumped: _____ CB Checked: _____
											Clear Roots Solids Grease Debris MAP # _____ Structural Defect Poor Hydraulics Unknown CB Pumped: _____ CB Checked: _____
											Clear Roots Solids Grease Debris MAP # _____ Structural Defect Poor Hydraulics Unknown CB Pumped: _____ CB Checked: _____

TOTAL MAINS CLEANED: 135.0 metres	TOTAL FLUSHED: 135.0 metres	CB'S INSPECTED	CB'S PUMPED:
WEATHER Road Surface Wet <input type="checkbox"/> Road Surface Dry <input checked="" type="checkbox"/>	TOTAL ROOT CUT: 135.0 metres	AREA MAP NO: Q21	LEADS FLUSHED:


OPERATOR IV: P. SARAZIN WORKING SUPERVISOR II: _____
OPERATOR II: K. TAYLOR TRUCK DRIVER I: _____

* If a Sanitary or Combined Sewer main is blocked and flooding, please use a Crew Report to record the incident.

Work Slip

SAP Charge #		Address & Location:				Responsible	
968810 968 751012		450 E 47 (481 E 48)				Sewer Operations	
Work Order #		Work Order Activity				Created Date	
		UNSTOP					
Group Project #		Problem		Sub Activity		Assigned To	Crew ID
						4171	35
Work Order Comments:							
St Andrews Parish - Gymnasium							
Reference #1						Billable?	
Reference #2		No Schedule					
Service Request #:		SR 968810					
Contact Name				Contact Phone		Contact Type	
Asset Type		Asset ID #	B.U.N	Status	Asset Area	Map # (Facet)	District
No Asset in Hansen						Q-20-21	
Asset Details:							
Safety & Asset Notes:							
PM Schedule		Last Completed Work Order					
Crew Comments							
Complete							
Work Completed Date: June 4, 2016				Print Name: M. Hoshowski		Crew ID: 35	

CONTACT: GRAHAM McVeigh		PHONE:	UNSTOP #: 31002
ADDRESS: 450 E. 47.		SCHEDULE #: SLB-PRST ISSUE	SIGNATURE: WITH <input type="checkbox"/> WITHOUT <input type="checkbox"/>
SCHEDULED DATE:	LAST COMPLETED: Nov 2014	INTERVAL: -	WO: FOR OFFICE USE
TIME STARTED: 8:00 pm	TIME FINISHED: 8:50 pm	Day After (Call)	STRAIGHT TIME _____ HRS
SUBFOREMAN: M. HOSHOVSKI	EMPLOYEES: D. Chim	CREW ID: 35	TRUCK: C1315
TASK:			CALL OUT TIME _____ HRS
UNSTOP <input checked="" type="checkbox"/>	CR PROGRAM <input type="checkbox"/>	TV INSPECTION <input type="checkbox"/>	TV FOR REUSE <input type="checkbox"/>
INSTALL C/O <input type="checkbox"/>	SPECIALS <input type="checkbox"/>	INVESTIGATION <input type="checkbox"/>	PLUGGED MAIN <input type="checkbox"/>
WORKED FROM:			OVERTIME _____ HRS
INSIDE <input type="checkbox"/>	C/O <input checked="" type="checkbox"/>	TOILET <input type="checkbox"/>	D/U <input type="checkbox"/>
OUTSIDE <input checked="" type="checkbox"/>	SUMP <input type="checkbox"/>	STACK <input type="checkbox"/>	
PRECONDITION WITH CCTV:			ACCESS LOCATION DETAILS: 1FO Building
GOOD <input checked="" type="checkbox"/>	FAIR <input type="checkbox"/>	POOR <input type="checkbox"/>	
REQUIRE TO CLEAN:			1/2 HR TRAVEL TIME INCL. <input type="checkbox"/>
YES <input type="checkbox"/>	NO <input checked="" type="checkbox"/>		TOTAL CHARGE \$ _____
DEFECT / BLOCKAGE:			FLUSH CONNECTION <input type="checkbox"/>
ROOTS:	DEBRIS <input type="checkbox"/>	COMB MAIN <input checked="" type="checkbox"/>	CR W SIGNATURE <input type="checkbox"/>
LIGHT <input type="checkbox"/>	GREASE <input type="checkbox"/>	METRO MAIN <input type="checkbox"/>	TV <input type="checkbox"/>
MEDIUM <input type="checkbox"/>	PONDING <input type="checkbox"/>		ADD TO CR PROGRAM:
HEAVY <input type="checkbox"/>	STRUCTURAL <input type="checkbox"/>		6 MTH <input type="checkbox"/>
SOLIDS <input type="checkbox"/>	OTHER: <input checked="" type="checkbox"/>		12 MTH <input type="checkbox"/>
AFTER CLEANING:			18 MTH <input type="checkbox"/>
GOOD <input type="checkbox"/>	FAIR <input type="checkbox"/>	POOR <input type="checkbox"/>	SCHEDULE DATE: _____
SOUND TEST:			HOLD CHARGING <input checked="" type="checkbox"/>
NO SOUND <input type="checkbox"/>	POOR <input type="checkbox"/>	GOOD <input checked="" type="checkbox"/>	RECOMMENDATIONS: _____
MAIN INSPECTION:			CHARGE <input type="checkbox"/>
VISUAL INSPECTION <input checked="" type="checkbox"/>			SHARE <input type="checkbox"/>
CLEANING REQUIRED <input type="checkbox"/>			NO CHARGE <input checked="" type="checkbox"/>
FLUSH <input type="checkbox"/>			APPROVED BY:
ROOT CUT <input type="checkbox"/>			INVOICE CANCELLED PER: _____
FROM MH#: 74.4			DATE CANCELLED: _____
TO MH#: toward 60.7			RECORDS: _____
DISPATCH: _____			

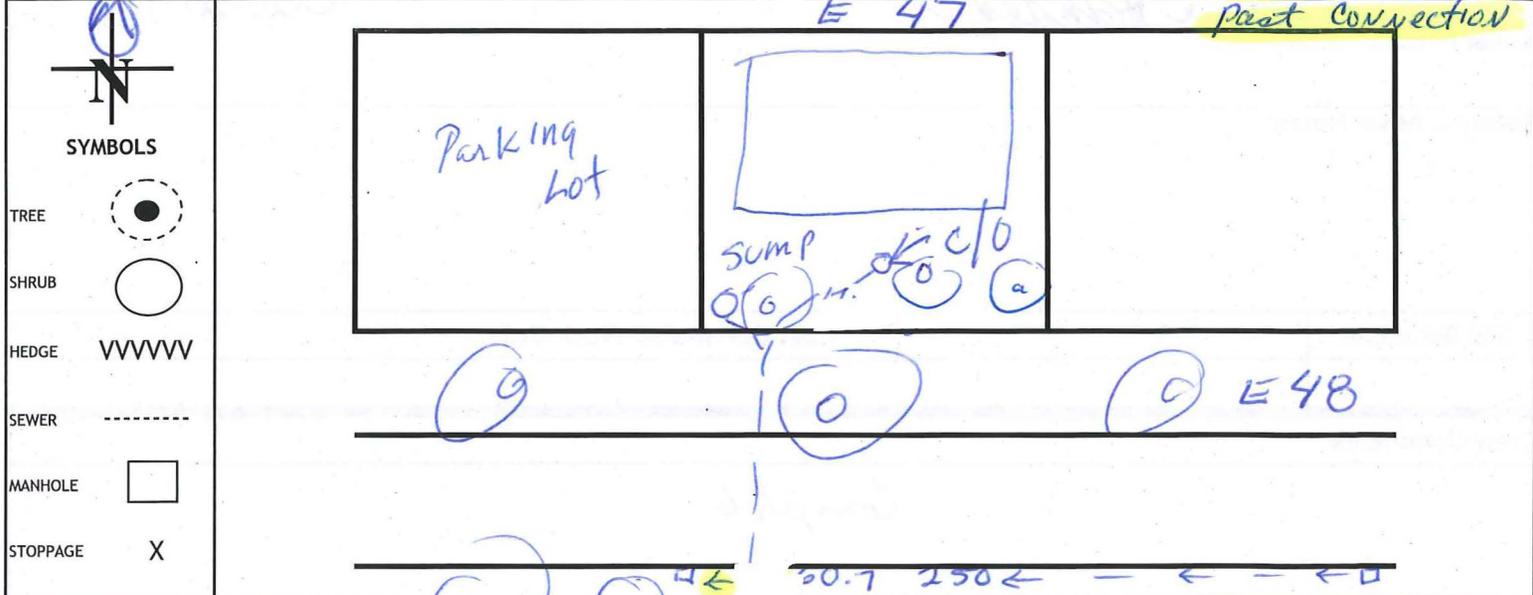

CONNECTION:	DEPTH AT PL: 0 M	PL IS 0 M FROM C/O	DEPTH AT MAIN: _____ M	WYE MEASUREMENTS:
PRIVATE SIDE RELAID: <input type="checkbox"/>	PL OFFSET: _____ M	N S E W of N S E W	DEPTH AT HOUSE: _____ M	_____ M
CITY SIDE RELAID: <input type="checkbox"/>				FROM DOWNSTREAM MH _____ M
COMMENTS: Complete was flowing				
Contractor was saying 3 floods recently with damage No visible problems abs - private side + PVC city side - tried to tv down sewer main couldn't reach 10m in main to man hole 74.4 we need to have camera crew to tv main from man hole 74.4 to East Past Connections may need to be root cut as a problem may exist				
SUPT COMMENTS: Created W/O 1235 751063 for CCTV - Report to T. Shaw				
				SUPT SIGNATURE:



Work Slip

SAP Charge #	Address & Location: 400 - 499 E 48TH AV (Crew to SCCTV main for condition of pipe and to see any remaining root infiltration - report to T. Shaw)			Responsible		
EES755116				Sewer Operations		
Work Order #	Work Order Activity			Created Date		
755116	Maintenance(400 E 48 CCTV 250 C main)			Jun 15, 2016		
Group Project #	Problem	Sub Activity	Assigned To	Crew ID		
		SCCTV	ALBANO LUIS	S_Crew23		
Work Order Comments:						
Reference #1	EES751012			Billable?		
Reference #2				N		
Service Request #:	R968810 (Sewage Backup/Flooding)					
Contact Name		Contact Phone	Contact Type			
McVeigh Mechanical		604-808-4218	Other			
Asset Type	Asset ID #	B.U.N	Status	Asset Area	Map # (Facet)	District
Main (C)	401780		IN_SERVICE	CBD08	Q21	5
Asset Details: C 250 Millimeter VC 60.66 Meters 4.81% [60.66 - 250 C VC 4.81% 1930]:						
Safety & Asset Notes: <i>Sched 22746</i>						
PM Schedule	Last Completed Work Order					
	Jun 15, 2016; 753149; Maintenance (400 E 48 RC main)					
Crew Comments						
<p><i>Completed</i></p> <p><i>Should root cut annually whole Block</i></p> <p><i>all is good now. See Videos E+W of MH 74.4</i></p> <p><i>Could not access mh 24.7 T/D Both ways from MH 74.7</i></p>						
Work Completed Date:	<i>June 29 2016</i>	Print Name:	<i>M HOSKOWSKI</i>	Crew ID:	<i>23</i>	

TO EAST
from manhole 74.7 TO EAST
22. m man hole

24.7 + 60.7


30m. wye for 481 & 48
Property in Report.

TO West

Work Slip

SAP Charge #	Address & Location: 450 E 47TH AV			Responsible		
EES755112	ST ANDREWS SCHOO (No Asset in Hansen - Crew to CCTV connection for condition of pipe and location of root infiltration. Work from o/s sump - connection goes to E 48th 250 Comb Main)			Sewer Operations		
Work Order #	Work Order Activity			Created Date		
755112	Maintenance(450 E 47 - SCCTV SVCLN)			Jun 15, 2016		
Group Project #	Problem	Sub Activity	Assigned To	Crew ID		
		SCCTV	ALBANO LUIS	S_Crew23		
Work Order Comments:						
<i>Please trace. for hansen.</i>						
Reference #1				Billable?		
Reference #2				N		
Service Request #:	R968810 (Sewage Backup/Flooding)					
Contact Name		Contact Phone	Contact Type			
McVeigh Mechanical		604-808-4218	Other			
Asset Type	Asset ID #	B.U.N	Status	Asset Area	Map # (Facet)	District
Asset Details:						
Safety & Asset Notes:						
PM Schedule	Last Completed Work Order					
Crew Comments						
<i>Depth @ Wye 2.74 .. flowing + measured to E48 from wye 6.5 Building Gymnasium</i> <i>Bm. 55 m 481 E 48</i> <i>PL offset 34.1 W of E</i> <i>PL 15 14 m from C/O</i> <i>Measurements from Sani C/O 14m to P/L</i> <i>Storm Sump is 10' Deep.</i> <i>Depth @ PL 2.84 sani</i>						
Work Completed Date:	<i>June 29, 2016</i>	Print Name:	<i>MHOSKOWSKI</i>	Crew ID:	<i>23</i>	


E47th

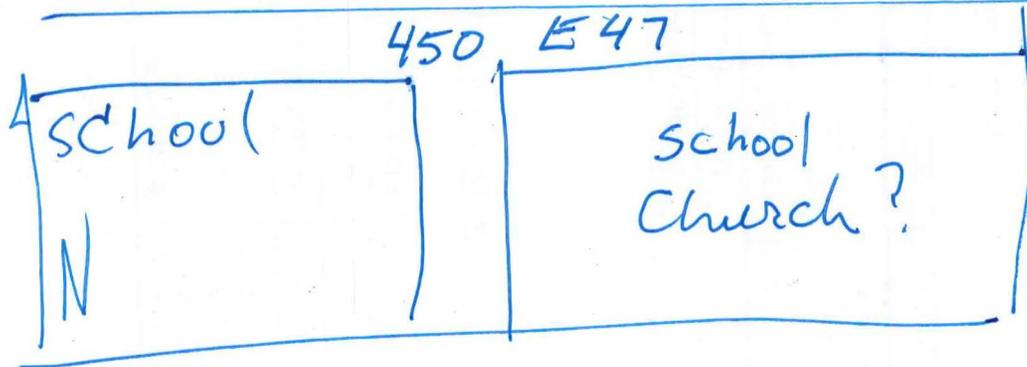

LS E47

LE
Prince Edward

Parking Lot
Play ground

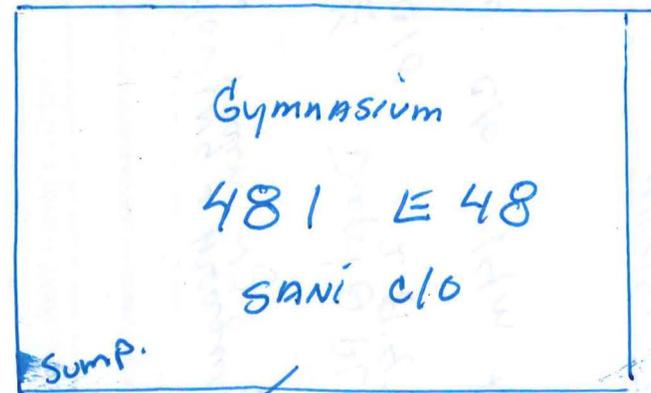

E48

22748

22747

22746



Wye 6.5

Bm 55

TVD & Recorded
