

File No.: 04-1000-20-2021-489

November 2, 2021

s.22(1)

Dear s.22(1)

Re: **Request for Access to Records under the Freedom of Information and Protection of Privacy Act (the "Act")**

I am responding to your request of September 20, 2021 for:

Engineering records regarding road and bike lane closures in the vicinity of the intersection of Burrard Street and Harwood Street on or about April 19, 2017*.

***Related to a motor vehicle accident on that date.**

All responsive records are attached.

Under section 52 of the Act, and within 30 business days of receipt of this letter, you may ask the Information & Privacy Commissioner to review any matter related to the City's response to your FOI request by writing to: Office of the Information & Privacy Commissioner, info@oipc.bc.ca or by phoning 250-387-5629.

If you request a review, please provide the Commissioner's office with: 1) the request number (#04-1000-20-2021-489); 2) a copy of this letter; 3) a copy of your original request; and 4) detailed reasons why you are seeking the review.

Yours truly,

[Signature on file]

Barbara J. Van Fraassen, BA
Director, Access to Information & Privacy

Barbara.vanfraassen@vancouver.ca
453 W. 12th Avenue Vancouver BC V5Y 1V4

*If you have any questions, please email us at foi@vancouver.ca and we will respond to you as soon as possible. Or you can call the FOI Case Manager at 604.871.6584.


Encl.

:ag

From: Marion <mdegear@telus.net>
To: "Plant, Sherwood" <Sherwood.Plant@vancouver.ca>
"Nowak, Greg" <Greg.Nowak@vancouver.ca>
CC: "Currie, David" <David.Currie@vancouver.ca>
"Wilson, Sarah" <Sarah.Wilson@vancouver.ca>
"Hothi, Jasvinder" <Jasvinder.Hothi@vancouver.ca>
"Durnford, Jack" <Jack.Durnford@vancouver.ca>
Date: 4/18/2017 2:02:30 PM
Subject: BURRARD NORTH DAILY TMP REPORT - April 18

Good afternoon everyone,

Ansan (Marion DeGear) reviewed the Burrard & Pacific base TMP and noted all signs and markings were in the correct position at the start of the day.

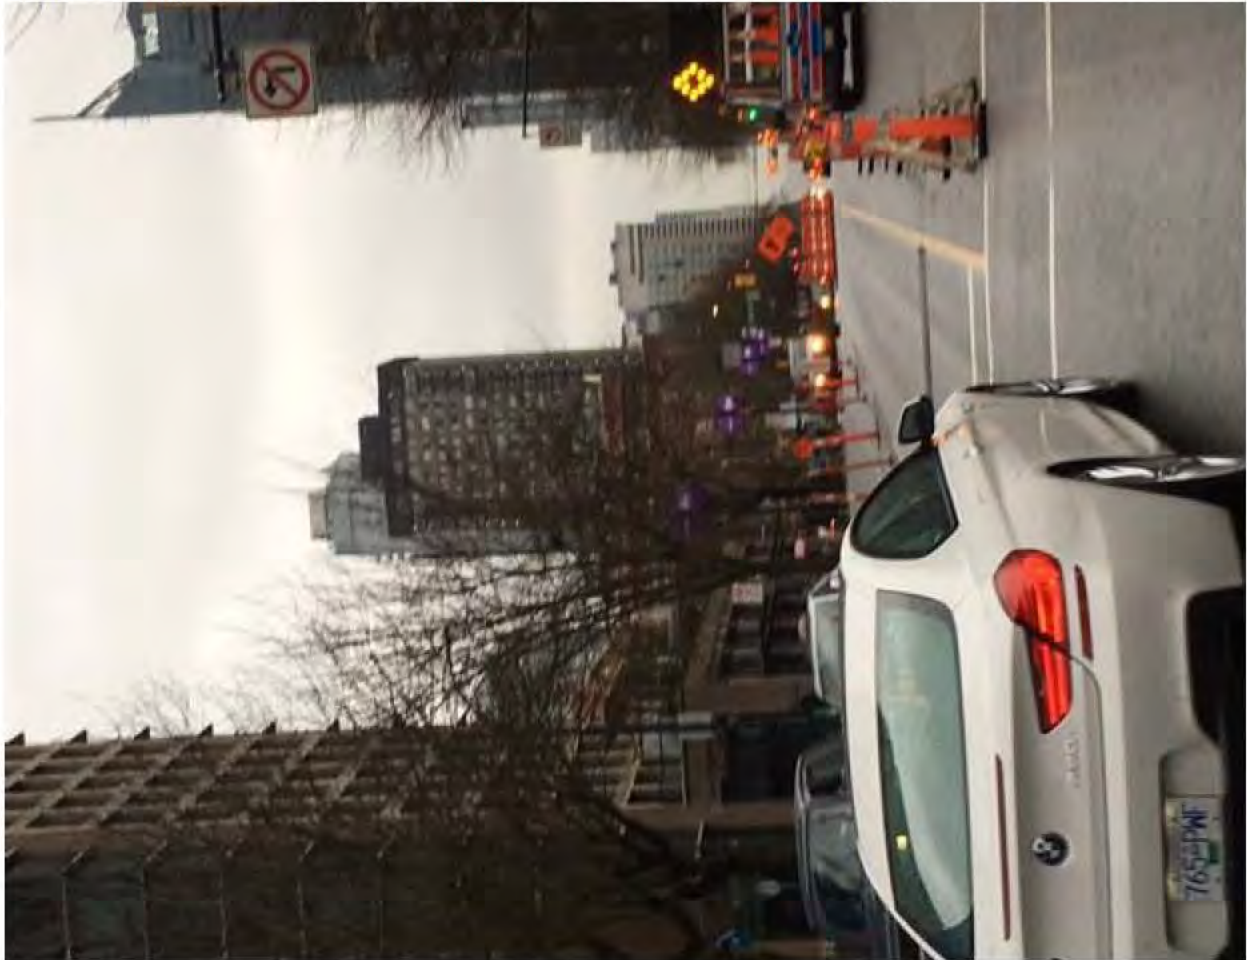

BURRARD - PACIFIC SE CORNER

Ansan (Marion DeGear) reviewed the days scope of work with sewer foreman (Tito) TCP's (Kerry & Tracey). Excavations continue for storm sewers, back fill, tamp, saw cutters on site for 10 o'clock to cut for mid block CB connect to M/H.







Modifications for Pacific base TMP are as follows:

- Pacific traffic is in a counterflow diversion in the westbound lanes from west of Burrard too east of Hornby.
- East bound bridge off ramp traffic has been diverted NW of the Construction site.
- Bike detour installed (own bike lane) along side of traffic.

West bound @ Hornby



North & East bound (off ramp diversion/bike detour)





East bound on pacific/ bike route detour



No modifications required for Burrard Base TMP.

BURRARD EAST SIDE - NORTH END

Ansan (Marion DeGear) reviewed today's scope of work with Streets concrete crew Forman (Marijan), it was discussed gradall will be on site continuing the excavation for east side sidewalk. Vactor to remove soil around 3 tree stumps for excavation.





If you require any further information or have any questions please call.

Thank you,


Marion Degear
ANSAN - LCS
C#. [604.306.0085](tel:604.306.0085)

Sent from my iPhone

From: Marion <mdegear@telus.net>
To: "Plant, Sherwood" <Sherwood.Plant@vancouver.ca>
"Nowak, Greg" <Greg.Nowak@vancouver.ca>
CC: "Currie, David" <David.Currie@vancouver.ca>
"Armendariz, Raul" <Raul.Armendariz@vancouver.ca>
"Wilson, Sarah" <Sarah.Wilson@vancouver.ca>
"Hothi, Jasvinder" <Jasvinder.Hothi@vancouver.ca>
"Durnford, Jack" <Jack.Durnford@vancouver.ca>
Date: 4/19/2017 1:31:46 PM
Subject: BURRARD NORTH DAILY TMP REPORT - April 19

Good afternoon everyone,

Ansan (Marion DeGear) reviewed the Burrard & Pacific base TMP and noted all signs and markings were in the correct position at the start of the day.

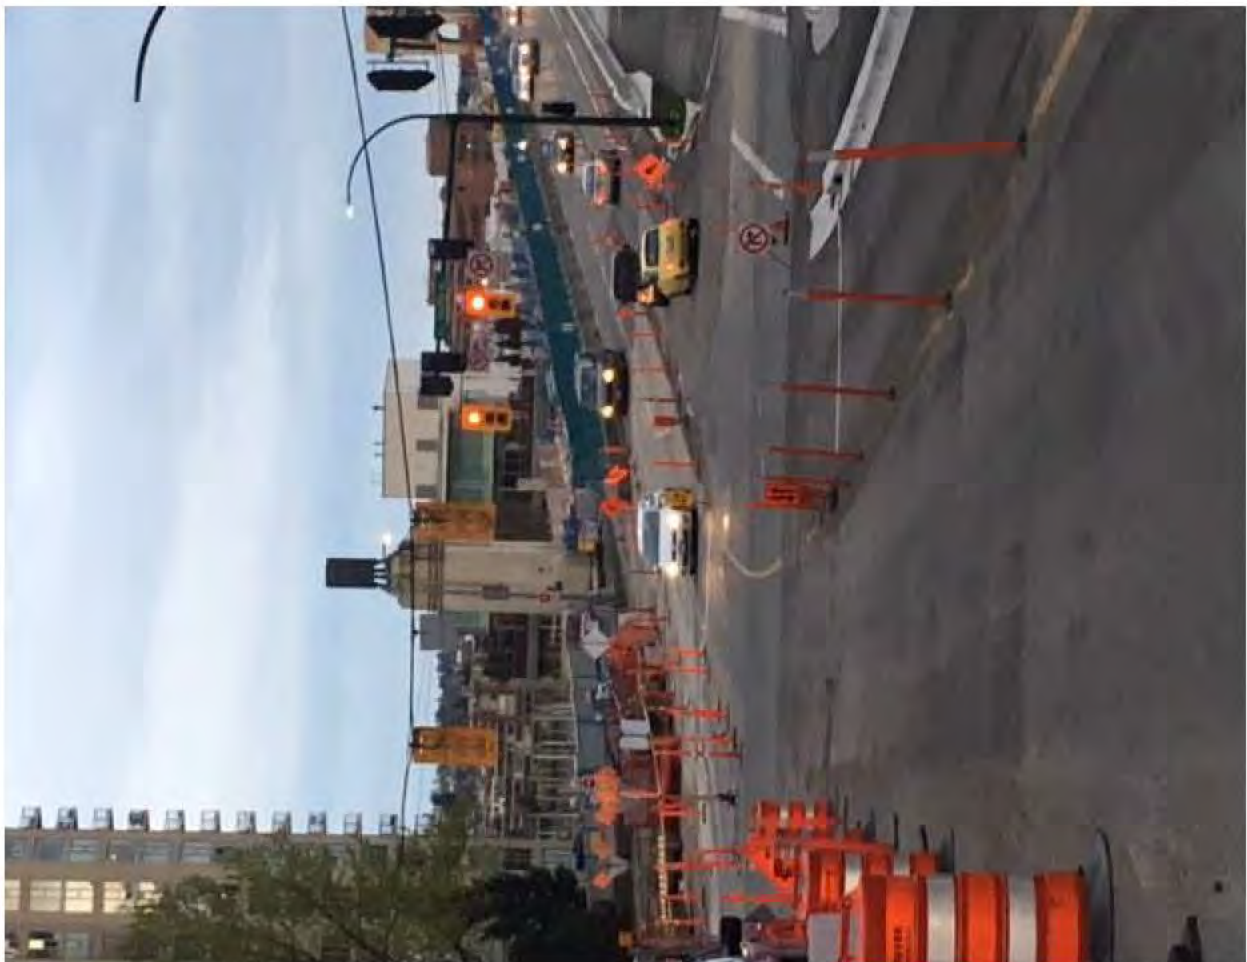

BURRARD - PACIFIC SE CORNER

Ansan (Marion DeGear) reviewed the days scope of work with sewer foreman (Tito) TCP's (Kerry & Tracey). Excavations (mainlining) continue for storm sewers, back fill, tamp & compaction testing.





BURRARD - PACIFIC SW CORNER

COV Parks board mobilized on site, Ansan spoke with Forman (Cyrus) it was discussed 18 new trees will be planted on the south side & the SW corner of Pacific.





Modifications for Pacific base TMP are as follows:



- Pacific traffic is in a counterflow diversion in the westbound lanes from west of Burrard too east of Hornby.
- East bound bridge off ramp traffic has been diverted NW of the Construction site.
- Bike detour installed (own bike lane) along side of traffic.
- cyclist & Pedestrians share a partial part of the sidewalk on the SW corner.



No modifications required for Burrard Base TMP.



BURRARD EAST SIDE - NORTH END

Ansan (Marion DeGear) reviewed today's scope of work with Streets concrete crew Forman (Marijan), it was discussed material will be added to trench, tamped, sidewalk to be formed, concrete (broomed) pour.






If you require any further information or have any questions please call.

Thank you,


Marion Degear
ANSAN - LCS
C#. [604.306.0085](tel:604.306.0085)


Sent from my iPhone

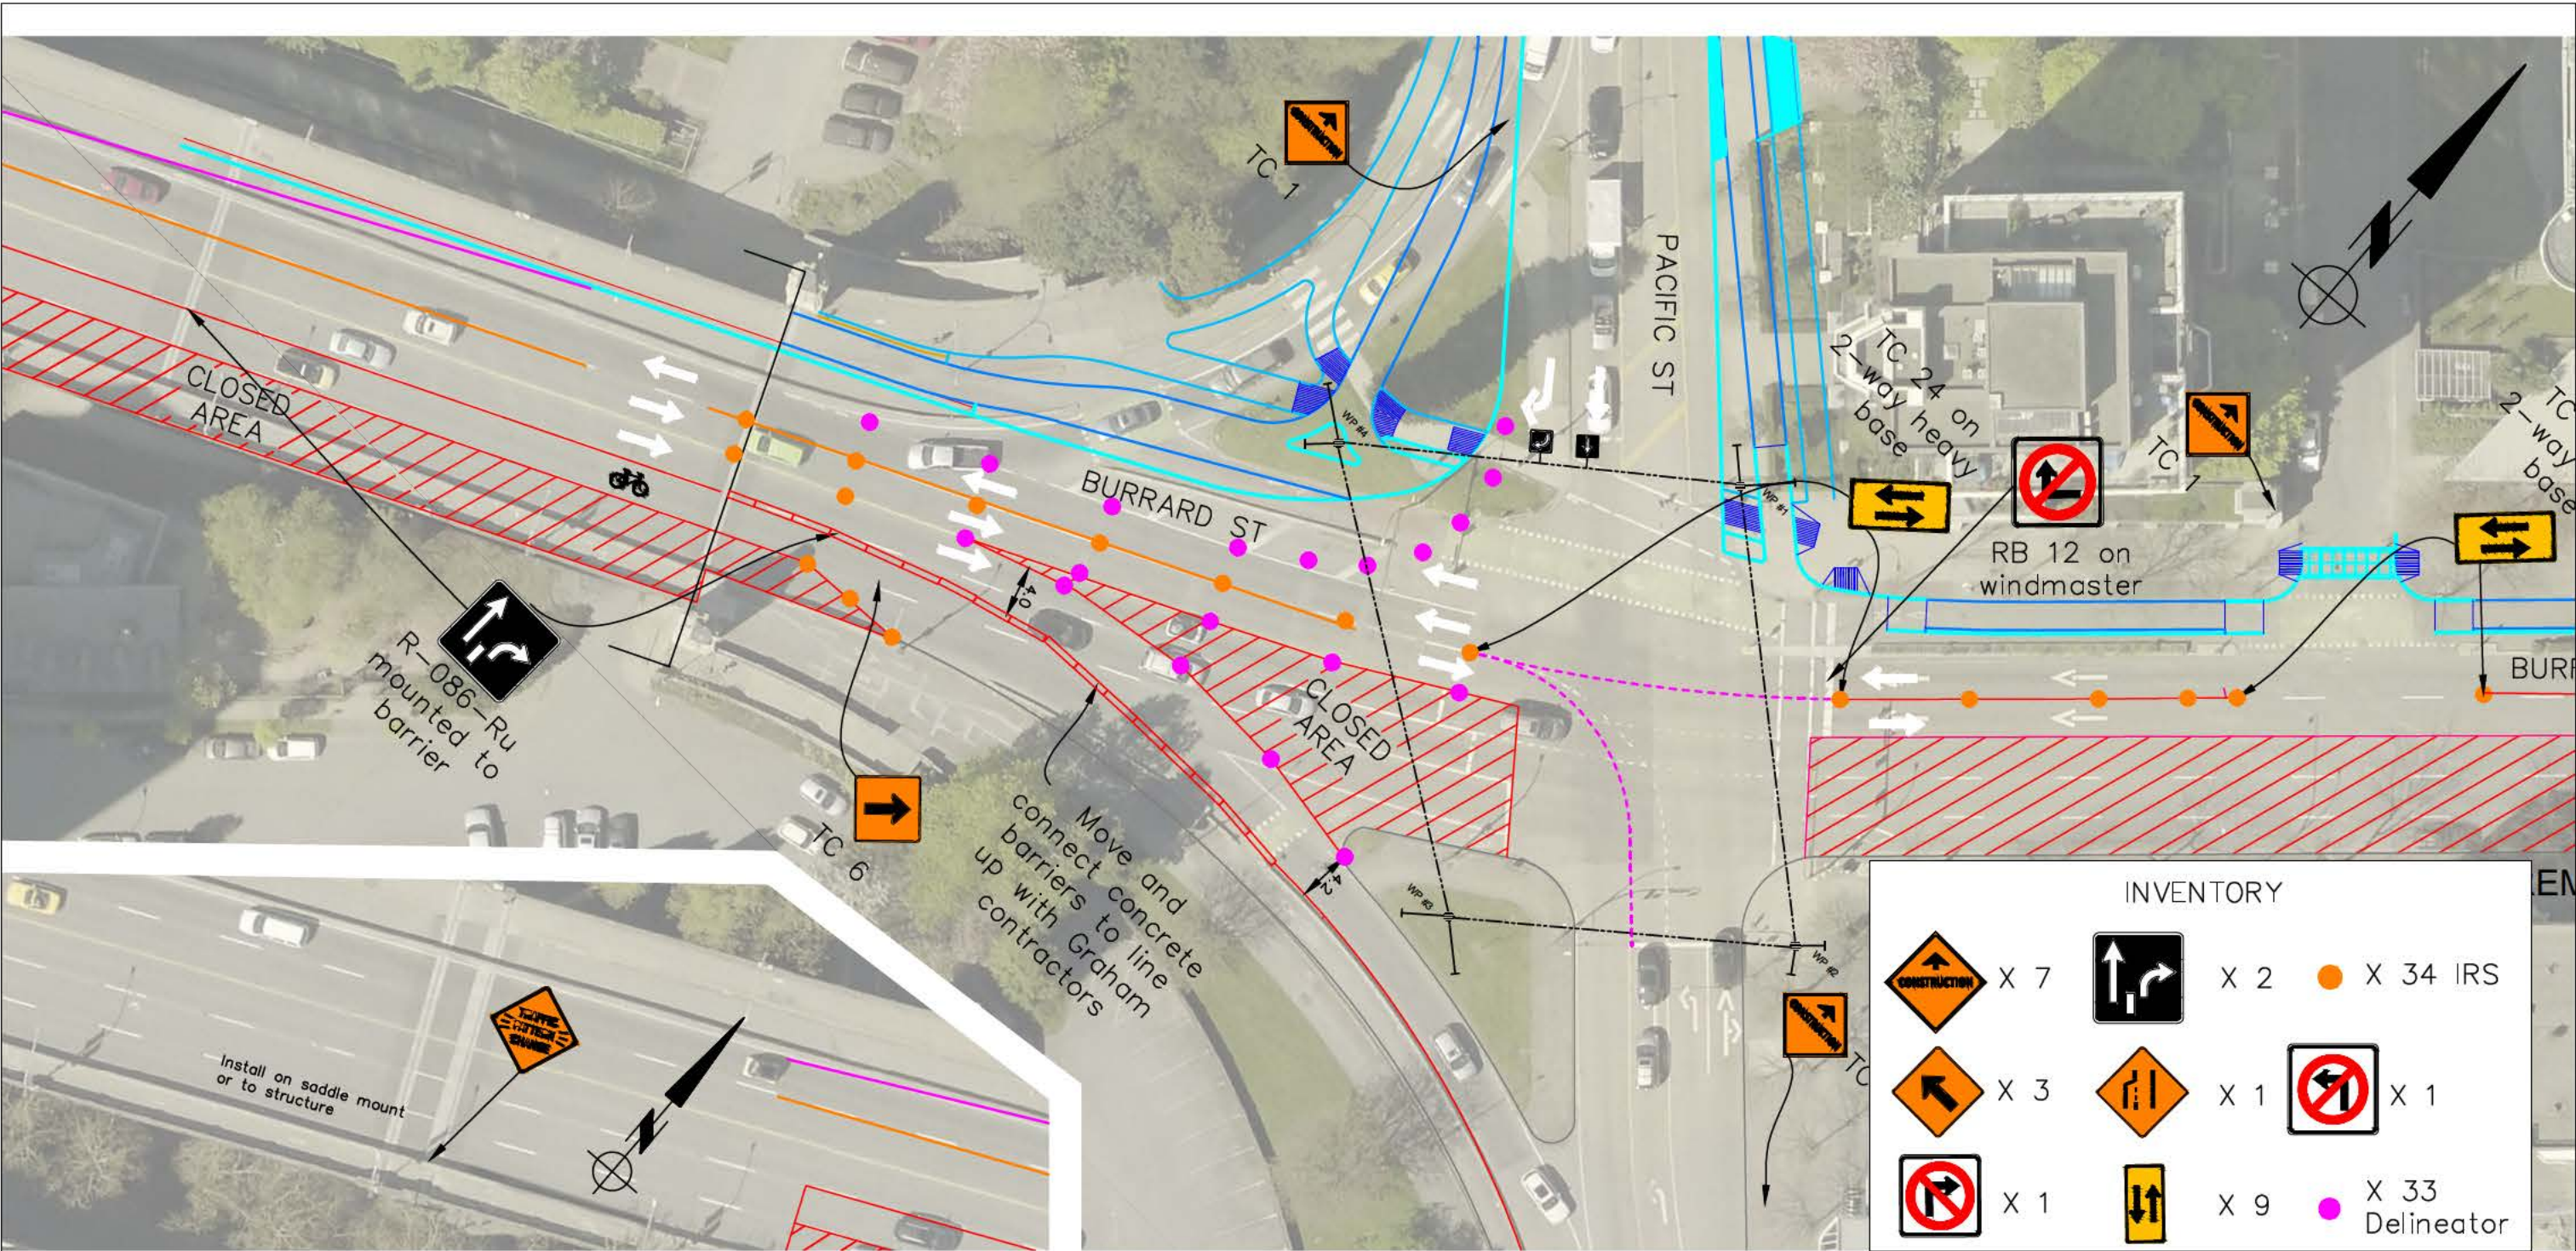


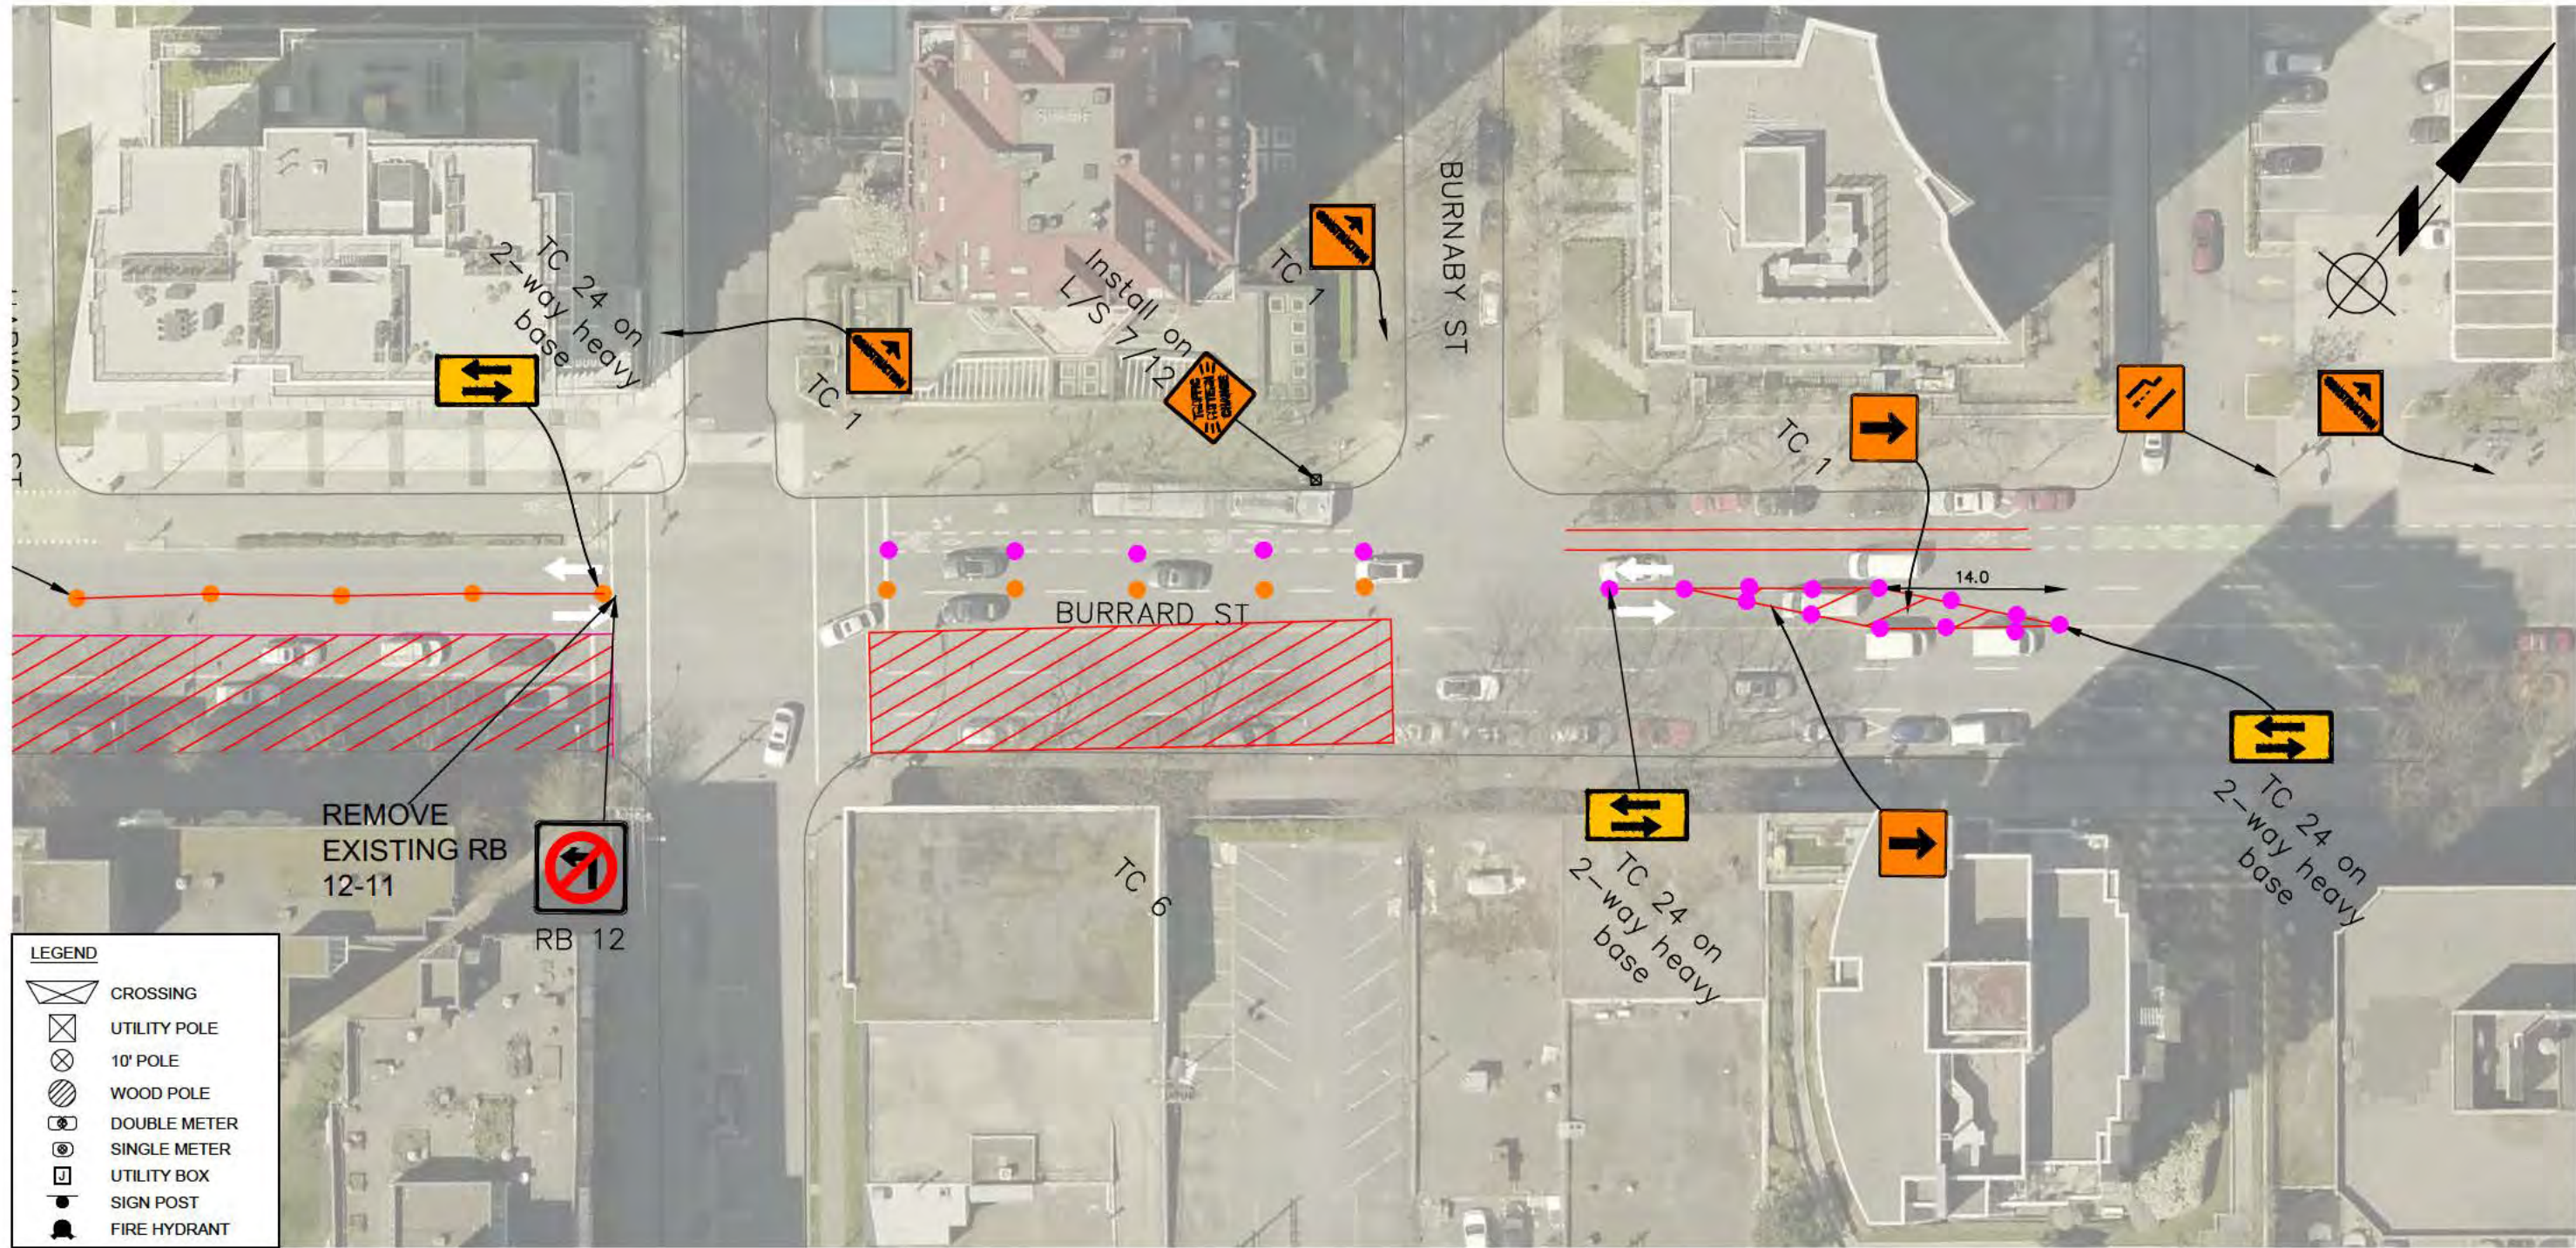
NOTES
GLUE DOWN OR IRS DELINEATOR AND 2 WAY SIGNS. CONSTRUCTION WARNING TO BE MOUNTED ON WINDMASTER OR TO PERMANENT POLES

DIRECTOR OF TRANSPORTATION	DATE	DATE
TRANSPORTATION DESIGN	DATE	ENGINEER OF RECORD
TRANSPORTATION PLANNING	DATE	DESIGNER
TRAFFIC AND DATA MANAGEMENT	DATE	DRAFTER
PARKING MANAGEMENT	DATE	CHECKER

 ENGINEERING SERVICES TRANSPORTATION DIVISION				VANDocs NUMBER	
ENG - TDM - TRAFFIC MANAGEMENT PLAN - BURRARD AND PACIFIC				PROJECT NUMBER	
				FILE PATH	
				REFERENCE(S)	
BIKE FACILITIES YES <input type="checkbox"/> NO <input type="checkbox"/>	BUS ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	TRUCK ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	RAILWAY CROSSING YES <input type="checkbox"/> NO <input type="checkbox"/>	SCALE	SHEET-SET 1 OF 3

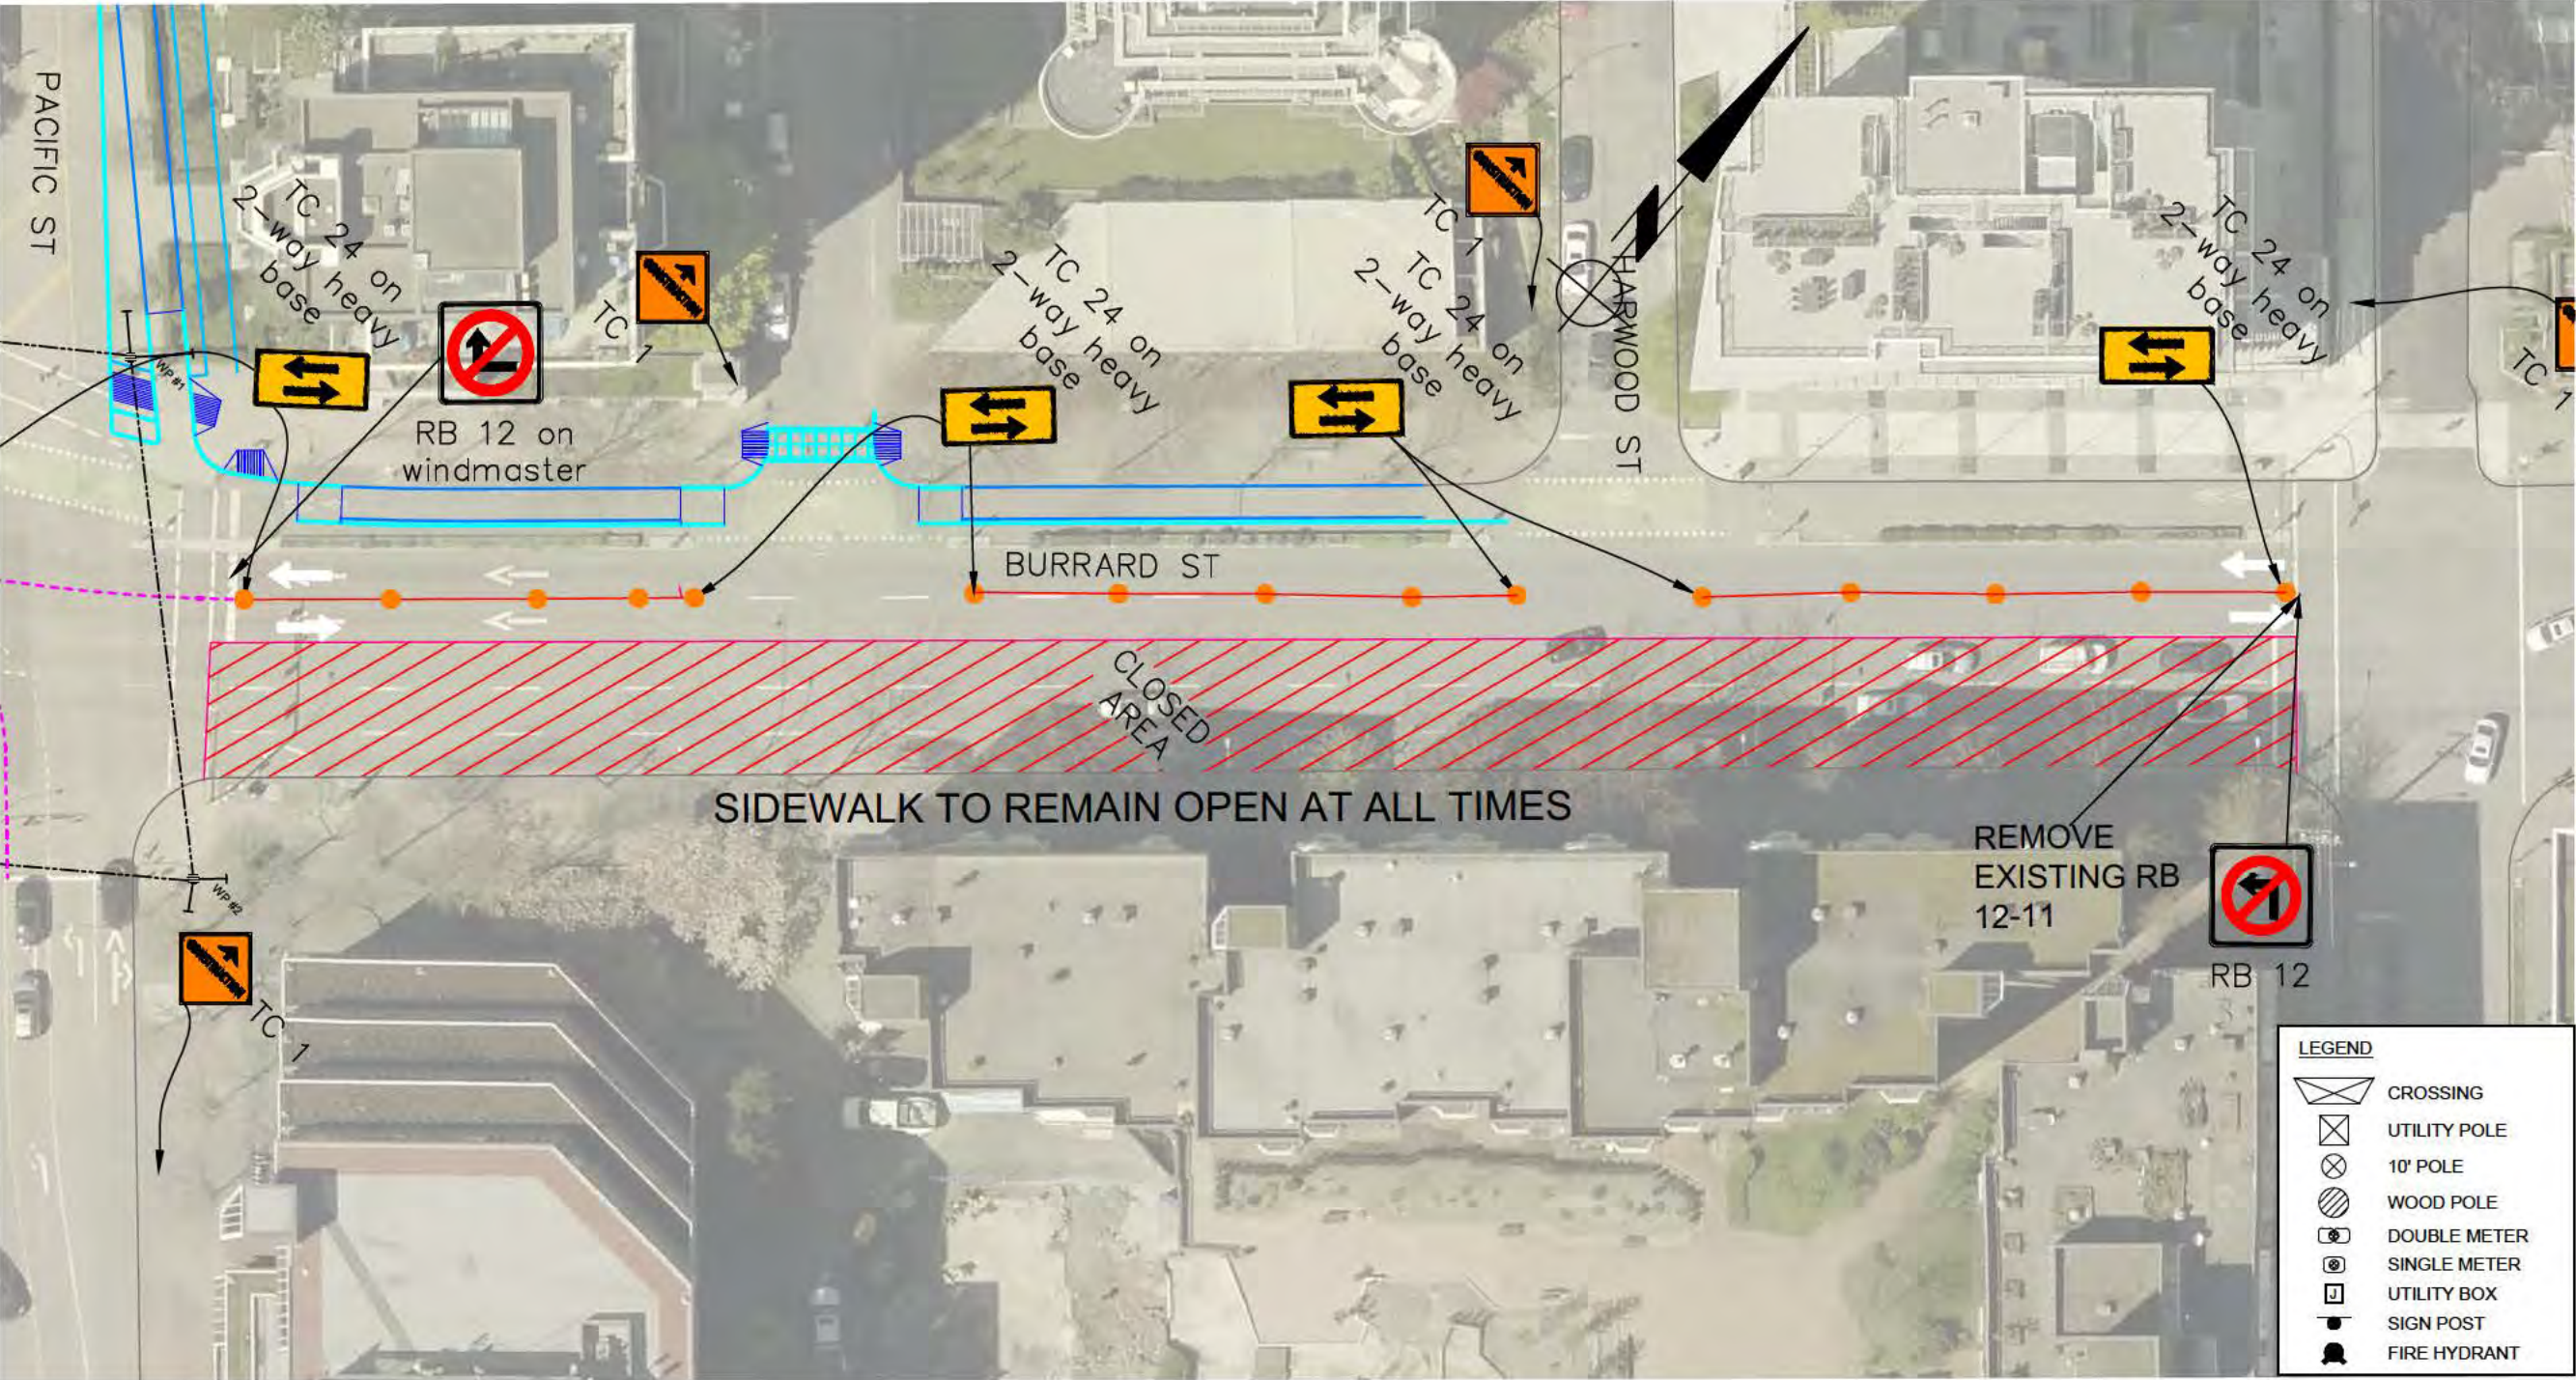


NOTES								VANDocs NUMBER	
GLUE DOWN OR IRS DELINEATOR AND 2 WAY SIGNS. CONSTRUCTION WARNING TO BE MOUNTED ON WINDMASTER OR TO PERMANENT POLES		DIRECTOR OF TRANSPORTATION	DATE	DATE	 ENGINEERING SERVICES TRANSPORTATION DIVISION				PROJECT NUMBER
		TRANSPORTATION DESIGN	DATE	ENGINEER OF RECORD					FILE PATH
		TRANSPORTATION PLANNING	DATE	DESIGNER	ENG - TDM - TRAFFIC MANAGEMENT PLAN - BURRARD AND HARWOOD				REFERENCE(S)
		TRAFFIC AND DATA MANAGEMENT	DATE	DRAFTER					
		PARKING MANAGEMENT	DATE	CHECKER					
				BIKE FACILITIES YES <input type="checkbox"/> NO <input type="checkbox"/>		BUS ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	TRUCK ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	RAILWAY CROSSING YES <input type="checkbox"/> NO <input type="checkbox"/>	SCALE
								SHEET-SET 2 OF 3	



NOTES
GLUE DOWN OR IRS DELINEATOR AND 2 WAY SIGNS. CONSTRUCTION WARNING TO BE MOUNTED ON WINDMASTER OR TO PERMANENT POLES

DIRECTOR OF TRANSPORTATION	DATE	DATE
TRANSPORTATION DESIGN	DATE	ENGINEER OF RECORD
TRANSPORTATION PLANNING	DATE	DESIGNER
TRAFFIC AND DATA MANAGEMENT	DATE	DRAFTER
PARKING MANAGEMENT	DATE	CHECKER

<div><div>ENGINEERING SERVICES TRANSPORTATION DIVISION</div></div> <div>ENG - TDM - TRAFFIC MANAGEMENT PLAN - BURRARD AND BURNABY</div>	VANDocs NUMBER			
	PROJECT NUMBER			
	FILE PATH			
	REFERENCE(S)			
BIKE FACILITIES YES <input type="checkbox"/> NO <input type="checkbox"/>	BUS ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	TRUCK ROUTE YES <input type="checkbox"/> NO <input type="checkbox"/>	RAILWAY CROSSING YES <input type="checkbox"/> NO <input type="checkbox"/>	SCALE
SHEET-SET 3 OF 3				

From: "Armendariz, Raul" <Raul.Armendariz@vancouver.ca>
To: "Currie, David" <David.Currie@vancouver.ca>
"Wilson, Sarah" <Sarah.Wilson@vancouver.ca>
"Durnford, Jack" <Jack.Durnford@vancouver.ca>
"Bevilacqua, Mario" <mario.bevilacqua@vancouver.ca>
"Clark, Kevin" <Kevin.Clark@vancouver.ca>
"Borger, Ron" <ron.borger@vancouver.ca>
"Brown, Ken" <ken.brown@vancouver.ca>
"Elford, Dan" <dan.elford@vancouver.ca>
"Durfee, Steven" <Steven.Durfee@vancouver.ca>
"Van Veen, Kyle" <Kyle.Vanveen@vancouver.ca>
"Zhou, Roy" <Roy.Zhou@vancouver.ca>
"Ledo, George" <George.Ledo@vancouver.ca>
"Plant, Sherwood" <Sherwood.Plant@vancouver.ca>
"Hatton, Rommel" <Rommel.Hatton@vancouver.ca>
"Goodlet, David" <David.Goodlet@vancouver.ca>
"Nilsson, Brad" <brad.nilsson@vancouver.ca>
"Storer, Paul" <paul.storer@vancouver.ca>
"Chou, Winston" <winston.chou@vancouver.ca>
"Wong, Donny" <donny.wong@vancouver.ca>
"Schwark, Mark" <mark.schwark@vancouver.ca>
"Marion Degear \"(mdegear@telus.net)\" <mdegear@telus.net>
"Moore, Doug" <doug.moore@vancouver.ca>
"Lester Marr" <marrl@ae.ca>
"Nguyen, Do" <do.nguyen@vancouver.ca>
"Newell, Chris" <Chris.Newell@vancouver.ca>
"Hothi, Jasvinder" <Jasvinder.Hothi@vancouver.ca>
"Porra, Aldo" <Aldo.Porra@vancouver.ca>
"Lina Maria Largo" <lina@isiltd.ca>
"Duane Neufeld" <neufeldd@ae.ca>
"Brach, Jas" <jas.brach@vancouver.ca>
"Hsu, Henry" <Henry.Hsu@vancouver.ca>
"Broderick, Fergal" <Fergal.Broderick@vancouver.ca>
Date: 4/27/2017 8:03:42 AM
Subject: For review - Burrard & Pacific Intersection - April 25, 2016 - Weekly Coordination Meeting - Draft Minutes
Attachments: ENG - PMO - BURRARD PACIFIC MEETING MINUTES #63 - April 25 2017.pdf

Good morning everyone:

Please find attached the minutes from Tuesday's meeting.

Please let me know of any errors or omissions.

Thank you.

Raul Armendariz, B.Eng.
Engineering Assistant IV - Project Coordinator
Project Delivery Branch - Cross Roads 7th floor
City of Vancouver - Engineering Services
507 W Broadway, Vancouver, V5Z 0B4
Ph: [604 873-7394](tel:6048737394) - Cel: [604 347-8580](tel:6043478580)
raul.armendariz@vancouver.ca
Web: www.vancouver.ca



Green Operations

The information in this email, and any files transmitted with it, is confidential and may be legally privileged. This message, including any attachments, is intended only for the person or entity to which it is addressed and may contain proprietary or confidential information. If you are intended recipient, be aware that your use of any confidential or personal information may be restricted by state and federal privacy laws. If you are not the intended recipient, you are not authorized to read, print, retain copy, disseminate, distribute, or forward this message or any part of it. If you have received this email in error, please notify the sender immediately and delete the material from any computer. Thank you.

Please consider the environment before printing this e-mail

MINUTES

BURRARD & PACIFIC INTERSECTION SAFETY IMPROVEMENTS

Meeting #63

April 25, 2017 10:00 AM – 10:30 AM

Streets Site Trailer at Pacific and Howe Intersection

Attendees: Jack Durnford, Kevin Clark, Steve Durfee, Ron Borger, George Ledo, Marion DeGear (ANSAN), Dave Currie, Sarah Wilson, Raul Armendariz.

<p>1. Safety and Construction Coordination</p> <p>.1 Onsite safety</p> <p>.1 Any observations by ISI are addressed immediately by the foreman.</p> <p>.2 Sewers Operations has been requested to remove worn traffic barricades from site.</p> <p>.3 Streets Operations will order new traffic barricades and charge the purchase cost to the project safety account.</p> <p>.4 City will send minutes to Lina M. Largo every week to keep her informed of crews working on site.</p> <p>.2 Coordination with other sites</p> <p>.1 Graham</p> <p>.1 Graham's work site will be fairly static over the next few months.</p> <p>.2 Drake Street – Traffic Ops</p> <p>.1 Traffic Operations to re-install permanent signing.</p> <p>.3 BC Hydro</p> <p>.1 FTC (Fred Thompson Contracting) to schedule the remaining work at the NW corner of Pacific St and Hornby St, once the existing street light pole and the Fire Hydrant at this location are relocated, as these utilities are in conflict with BC Hydro's ducting work. The fire Hydrant relocation is expected to begin Friday May 12th (during Phase 8) and will take up to 6 days to install the two Hydrants.</p> <p>.2 BC Hydro to relocate a pole at the south east corner of Drake St and Burrard St. Raul A. emailed BC Hydro in regard to this installation but we are still waiting for a responds with a schedule of this installation.</p> <p>.4 BMO Run (Sunday May 7th)</p> <p>.1 Crews were informed that this run will be taking place on Sunday May 7th. All work taking place on Pacific St to be protected with a fence and the road to the swept clear of any debris.</p> <p>.2 Operations to review any temporary cut repairs to ensure an even profile.</p>	<p>Lina M. Largo</p> <p>David C.</p> <p>Dan Elford</p> <p>Raul A.</p> <p>Ron Borger George Ledo Kevin Clark</p>
--	---

<p>2. Traffic Management</p> <p>.1 Current and upcoming TMPs</p> <p>.1 1300 & 1200 Block Burrard – East Side Construction TMP</p> <ol style="list-style-type: none"> 1. The TMP is modified daily to accommodate the construction needs of the day and returns to the TMP approved by TDM by the end of the day. 2. TDM has provided detailed construction TMPs for the Sewers and Streets construction on the north and south side of Pacific St. <p>.2 Daily Reporting of TMP Condition</p> <p>.1 ANSAN will continue to provide daily reports by e-mail to the City (to Jas, Kyle, Dave, Raul, Jack, Sherwood Plant and Greg Nowak).</p> <p>.2 The ANSAN report is to confirm that the Burrard North TCP has been reviewed by ANSAN, that the specified signing/coning was (or was not) in place and to report any adjustments to the TMP developed with the site foreman/foremen (if any) that day.</p>	<p>Marion DeGear</p> <p>Sherwood Plant, Greg Nowak</p> <p>Marion DeGear</p>
<p>3. Traffic Ops</p> <p>.1 Permanent markings and signing</p> <p>.1 Additional signing and markings will be installed as construction permits.</p> <p>.2 There are no permanent markings required until ST&E OB completes additional civil construction (currently 1300 Burrard).</p> <p>.3 The performance of the yellow guide markings installed in the Pacific St and Burrard St Intersection will continue to be monitored to determine if temporary paint markings are needed.</p> <p>.4 Raul A. provided an updated schedule to Dan Elford.</p> <p>.5 Transportation Design Branch requested to install the bike stencils on the west side of Burrard St. Raul A. sent a figure with the bike stencils that need to be installed to Dan Elford. This work will take place next week Friday night or Saturday during day, and is weather dependent.</p>	<p>Dan Elford Chris Newell Info</p> <p>Info</p> <p>Raul A.</p>
<p>4. Intersection of Pacific and Thurlow</p> <p>.1 1390 Thurlow – Retaining wall</p> <p>.1 Streets to complete minor finishing of the east end of the retaining wall.</p> <p>.2 Streets crews have remobilized to the Burrard North work site.</p>	<p>Ron Borger</p>
<p>5. Pacific – Burrard St to Hornby St (South side)</p> <p>.1 Sewer Crew</p> <p>.1 Sewers Operations will complete the PR. 250 mm storm, new MH D29, CB#17 & CB#20 by the end of Thursday April 27th.</p> <p>.2 The lead for CB#23 needs to be installed and trench to be paved before the sewers crews demobilize out of site.</p> <p>.3 The no post concrete barriers for the bike lane to be installed in</p>	<p>Jas Hothi Kyle Van Veen</p>

<p>the same alignment they were before sewers mobilized to site.</p> <p>.4 Steven D. to review with Sewer operations AE's compactions concern and to provide a response to AE (Linda Watkin – P. Eng.)</p>	Steven Durfee
<p>6. Pacific – Burrard St to Hornby St (North Side)</p> <p>.1 Water Crew</p> <p>.1 Fire Hydrant relocations are tentatively scheduled to start on Friday May 12th.</p> <p>.2 Sarah W. to clarify design with Water and AE.</p> <p>.2 Park Board</p> <p>.1 PB to remove several trees on Pacific St on Friday April 28th.</p> <p>.2 A notification letter will be delivered to business and house owners Wednesday April 26th.</p>	Henry Hsu Jas Brach
<p>7. 1300 Block Burrard (East Side)</p> <p>.1 Concrete Crew</p> <p>.1 The concrete crew poured some of the exposed aggregate concrete and broom finished concrete on the south portion of this block.</p> <p>.2 The inner and outer curb for the bike lane is being formed and will be placed the week of April 24th.</p> <p>.3 Excavation and forming for the bus pad to begin Thursday April 27th. Concrete placement to take place this weekend or the beginning of next week.</p> <p>.4 Ron B. to contact Out-Front Media when the installation of the bus shelter pad subgrade is prepared, as the rebar cage will need to be installed prior to concrete placement.</p> <p>.2 Electrical Crew</p> <p>.1 The new street light poles will be installed after the civil construction permits.</p> <p>.3 Civil Crew</p> <p>.1 The new conduit runs are being installed under the bike lane in the south half of this block.</p> <p>.2 The new concrete street light bases are being installed.</p> <p>.4 Water Crew</p> <p>.1 The DFPS hydrant will be installed once the custom pieces have arrived. Estimated time of arrival ~ 3 weeks.</p>	<p>Ron Borger Jack Durnford</p> <p>Kevin Clark</p> <p>George Ledo</p> <p>Fergal Broderick Jas Brach</p>
<p>8. 1200 block Burrard St (East side)</p> <p>.1 Civil Crew</p> <p>.1 Will mobilize to install ducting at the intersections of Drake St and Burrard St, and Burnaby St and Burrard St this coming Monday.</p> <p>.2 The Drake St and Burrard East side intersection may need to be closed a couple of times for this construction.</p> <p>.2 Paving Crew</p> <p>.1 To patch a few asphalt cuts before the concrete median can be installed.</p>	<p>George Ledo</p> <p>Jack Durnford Doug Moore</p> <p>Ron Borger</p>

<p>.3 Concrete Crew</p> <p>.1 Concrete crew to begin work this coming Tuesday.</p> <p>.2 The CB at the North East corner of Burrard St and Drake St will be set to final grade elevation once the concrete median is installed.</p>	
<p>9. Upcoming Survey Requirements</p> <p>.1 Roy Z to attend site to provide ongoing survey services at the east side of Burrard St between Pacific St and Drake St and on Pacific St east of Burrard St.</p> <p>.2 Operations will coordinate additional survey directly with Roy Z and with Sewers survey staff.</p>	Roy Zhou
<p>10. Archaeological Monitoring</p> <p>.1 Ongoing and upcoming monitoring</p> <p>.1 All crews continue to operate under chance find management protocol.</p>	Info
<p>11. Inspections / Testing / EoR Requirements</p> <p>.1 AE inspections</p> <p>.1 Streets Operations will repair minor damage to the C/G nose on SB Burrard immediately north of Pacific.</p> <p>.2 AE regular inspection will be required until further notice.</p> <p>.2 Testing</p> <p>.1 Last week's results.</p> <p>.1 Compaction test results were received for the week of April 17 and complied with CoV and AE requirements.</p> <p>.2 Some concerns were raised by AE in regards to the procedure for installing backfill material for the sewer work. Steven D. to review with Sewer operations AE's compactions concern and to provide a response to AE (Linda Watkin – P. Eng.)</p> <p>.2 Upcoming testing.</p> <p>.1 Testing required this week for compaction for the storm sewer and street works. Superintendents to coordinate with Kent Yard to ensure required testing occurs for Burrard North (AE design protocol) and Burrard North Downtown (City design protocol).</p>	<p>Info</p> <p>Steven Durfee</p> <p>Jas Hothi Ron Borger</p>

*Next Meeting: Tuesday, May 2, 2017

From: "Armendariz, Raul" <Raul.Armendariz@vancouver.ca>
To: "Currie, David" <David.Currie@vancouver.ca>
"Wilson, Sarah" <Sarah.Wilson@vancouver.ca>
"Durnford, Jack" <Jack.Durnford@vancouver.ca>
"Bevilacqua, Mario" <mario.bevilacqua@vancouver.ca>
"Clark, Kevin" <Kevin.Clark@vancouver.ca>
"Borger, Ron" <ron.borger@vancouver.ca>
"Brown, Ken" <ken.brown@vancouver.ca>
"Elford, Dan" <dan.elford@vancouver.ca>
"Durfee, Steven" <Steven.Durfee@vancouver.ca>
"Van Veen, Kyle" <Kyle.Vanveen@vancouver.ca>
"Zhou, Roy" <Roy.Zhou@vancouver.ca>
"Ledo, George" <George.Ledo@vancouver.ca>
"Plant, Sherwood" <Sherwood.Plant@vancouver.ca>
"Hatton, Rommel" <Rommel.Hatton@vancouver.ca>
"Tobiassen, Ryan" <Ryan.Tobiassen@vancouver.ca>
"Goodlet, David" <David.Goodlet@vancouver.ca>
"Nilsson, Brad" <brad.nilsson@vancouver.ca>
"Storer, Paul" <paul.storer@vancouver.ca>
"Chou, Winston" <winston.chou@vancouver.ca>
"Wong, Donny" <donny.wong@vancouver.ca>
"Schwark, Mark" <mark.schwark@vancouver.ca>
"Marion Degear \\\(mdegear@telus.net\\)" <mdegear@telus.net>
"Hothi, Jasvinder" <Jasvinder.Hothi@vancouver.ca>
"Durfee, Steven" <Steven.Durfee@vancouver.ca>
"Antoniazzi, Rob" <rob.antoniazzi@vancouver.ca>
"Ciccone, Christopher" <Christopher.Ciccone@vancouver.ca>
"Afonso, Gary" <Gary.Afonso@vancouver.ca>
"Newell, Chris" <Chris.Newell@vancouver.ca>
"Moore, Doug" <doug.moore@vancouver.ca>
"Porra, Aldo" <Aldo.Porra@vancouver.ca>
"Lee, Joyce \\\(ENG\\)" <joyce.w.lee@vancouver.ca>
"Marion Degear \\\(mdegear@telus.net\\)" <mdegear@telus.net>

Date: 4/24/2017 3:36:27 PM

Subject: For review - Burrard & Pacific Intersection - April 25, 2017 - Weekly Coordination Meeting - Draft Agenda/Site Map (Construction Update)

Attachments: ENG - PMO - BURRARD PACIFIC MEETING AGENDA #63 - Apr 25 2017.pdf
ENG - PMO - BURRARD PACIFIC Site Map Weekly Update #10 - April 25 2017.pdf

Good afternoon everyone:

Please find the following PDF files attached:

- ☐ The draft agenda #63 for tomorrow's meeting
- ☐ Site Map (Construction Update)

Kind Regards

Raul Armendariz, B.Eng.
Engineering Assistant IV - Project Coordinator
Project Delivery Branch - Cross Roads 7th floor
City of Vancouver - Engineering Services
507 W Broadway, Vancouver, V5Z 0B4
Ph: [604 873-7394](tel:6048737394) - Cel: [604 817-5331](tel:6048175331)
raul.armendariz@vancouver.ca
Web: www.vancouver.ca



The information in this email, and any files transmitted with it, is confidential and may be legally privileged. This message, including any attachments, is intended only for the person or entity to which it is addressed and may contain proprietary or confidential information. If you are intended recipient, be aware that your use of any confidential or personal information may be restricted by state and federal privacy laws. If you are not the intended recipient, you are not authorized to read, print, retain copy, disseminate, distribute, or forward this message or any part of it. If you have received this email in error, please notify the sender immediately and delete the material from any computer. Thank you.

 *Please consider the environment before printing this e-mail*

AGENDA

BURRARD & PACIFIC INTERSECTION SAFETY IMPROVEMENTS

Meeting #63

April 25th, 2017 10:00 AM – 11:00 AM

Streets Site Trailer at Pacific and Howe Intersection

1. Safety

- .1 Onsite safety
- .2 Coordination with other sites
 - .1 Graham
 - .2 BC Hydro (Pacific St – North Side)
 - .1 Fred Thomson Contracting to come back one more day to complete work on the NW corner of Hornby St and Pacific St.
 - .3 BMO RUN – Vancouver Marathon (Sunday May 7th)
 - .1 Course of the Race

2. Traffic Management

- .1 Current and upcoming TMPs
 - .1 TMP on Burrard
 - .1 Burrard at Pacific
 - .2 Daily report of TMP condition

3. Traffic Ops

- .1 Permanent & Temporary markings and signing
 - .1 The bike stencil needs to be installed on west side of Burrard St.

4. Pacific – Burrard to Hornby

- .1 Sewer Crew (South Side) – Progress and look ahead
 - .1 PR. 250 mm storm line ongoing
 - .2 CB#17 & CB#20
 - .3 MH D29 installation
 - .4 Demobilization expected by Apr 27
 - .5 Connection crew will return for remainder of storm works
- .2 Paving Crew (South East corner of Pacific St & Burrard St)
 - .1 Temporary paving
 - .2 Removal of no post concrete barriers
- .3 Water Operations (North Side)
 - .1 Fire hydrant relocations scheduled for early in Phase 8 (tentatively Friday May 12th, 2017)

<p>.4 Park Board Crew</p> <p>.1 Tree removal Friday April 28th.</p>
<p>5. 1300 Block Burrard (East Side)</p> <p>.1 Concrete Crew – Progress and look ahead</p> <p>.1 Bus Shelter rebar cage base (Out-front Media)</p> <p>.2 Civil-Electrical Crew – Progress and look ahead</p> <p>.3 Electrical Crew – Progress and look ahead</p> <p>.4 Water crew (DFPS) – special materials ordered</p> <p>.5 BC Hydro – Burrard/Drake pole relocation - schedule TBD</p> <p>.1 Waiting for a response from BC Hydro</p>
<p>6. 1200 Block Burrard (East Side)</p> <p>.1 Concrete Crew – look ahead</p>
<p>7. Upcoming Survey Requirements</p> <p>.1 Upcoming survey requirements</p>
<p>8. Archaeological Monitoring</p> <p>.1 Chance Find Management protocol in effect until further notice</p>
<p>9. Inspections / Testing / EoR Requirements</p> <p>.1 AE inspections</p> <p>.2 Testing</p> <p>.1 Last week's results</p> <p>.2 Upcoming testing</p>

*Next Meeting: May 2nd, 2017

CONSTRUCTION
UPDATE

Drake St
- The street is opened to car and bike traffic.

Note:
- Park Board planted trees the week of April 17 on the following locations:
+ West side of Burrard St.
+ North & South side of Pacific St, west of Burrard St.


Concrete Crew
- Crews are prepping for exposed aggregate and C&G placement at the South portion of Burrard St.
- Exposed aggregate and room finished concrete placed at the north portion of Burrard St.
Civil - Electrical Crew
- New conduit is being installed for the new street lights.
- New concrete bases are being installed.

Sewers Crew
- The crews to finish installation of the STM, CB's and MH by the end of the week of April 24th, 2017.

BC Hydro (FTC)
- The crews to return to the North West corner of Hornby St and Pacific St to finish installation of BCH ducting by the end of ~May 2017.

LEGEND

- CIVIL - ELECTRICAL
- SEWER
- CONCRETE
- PAVING
- WATER
- BC HYDRO

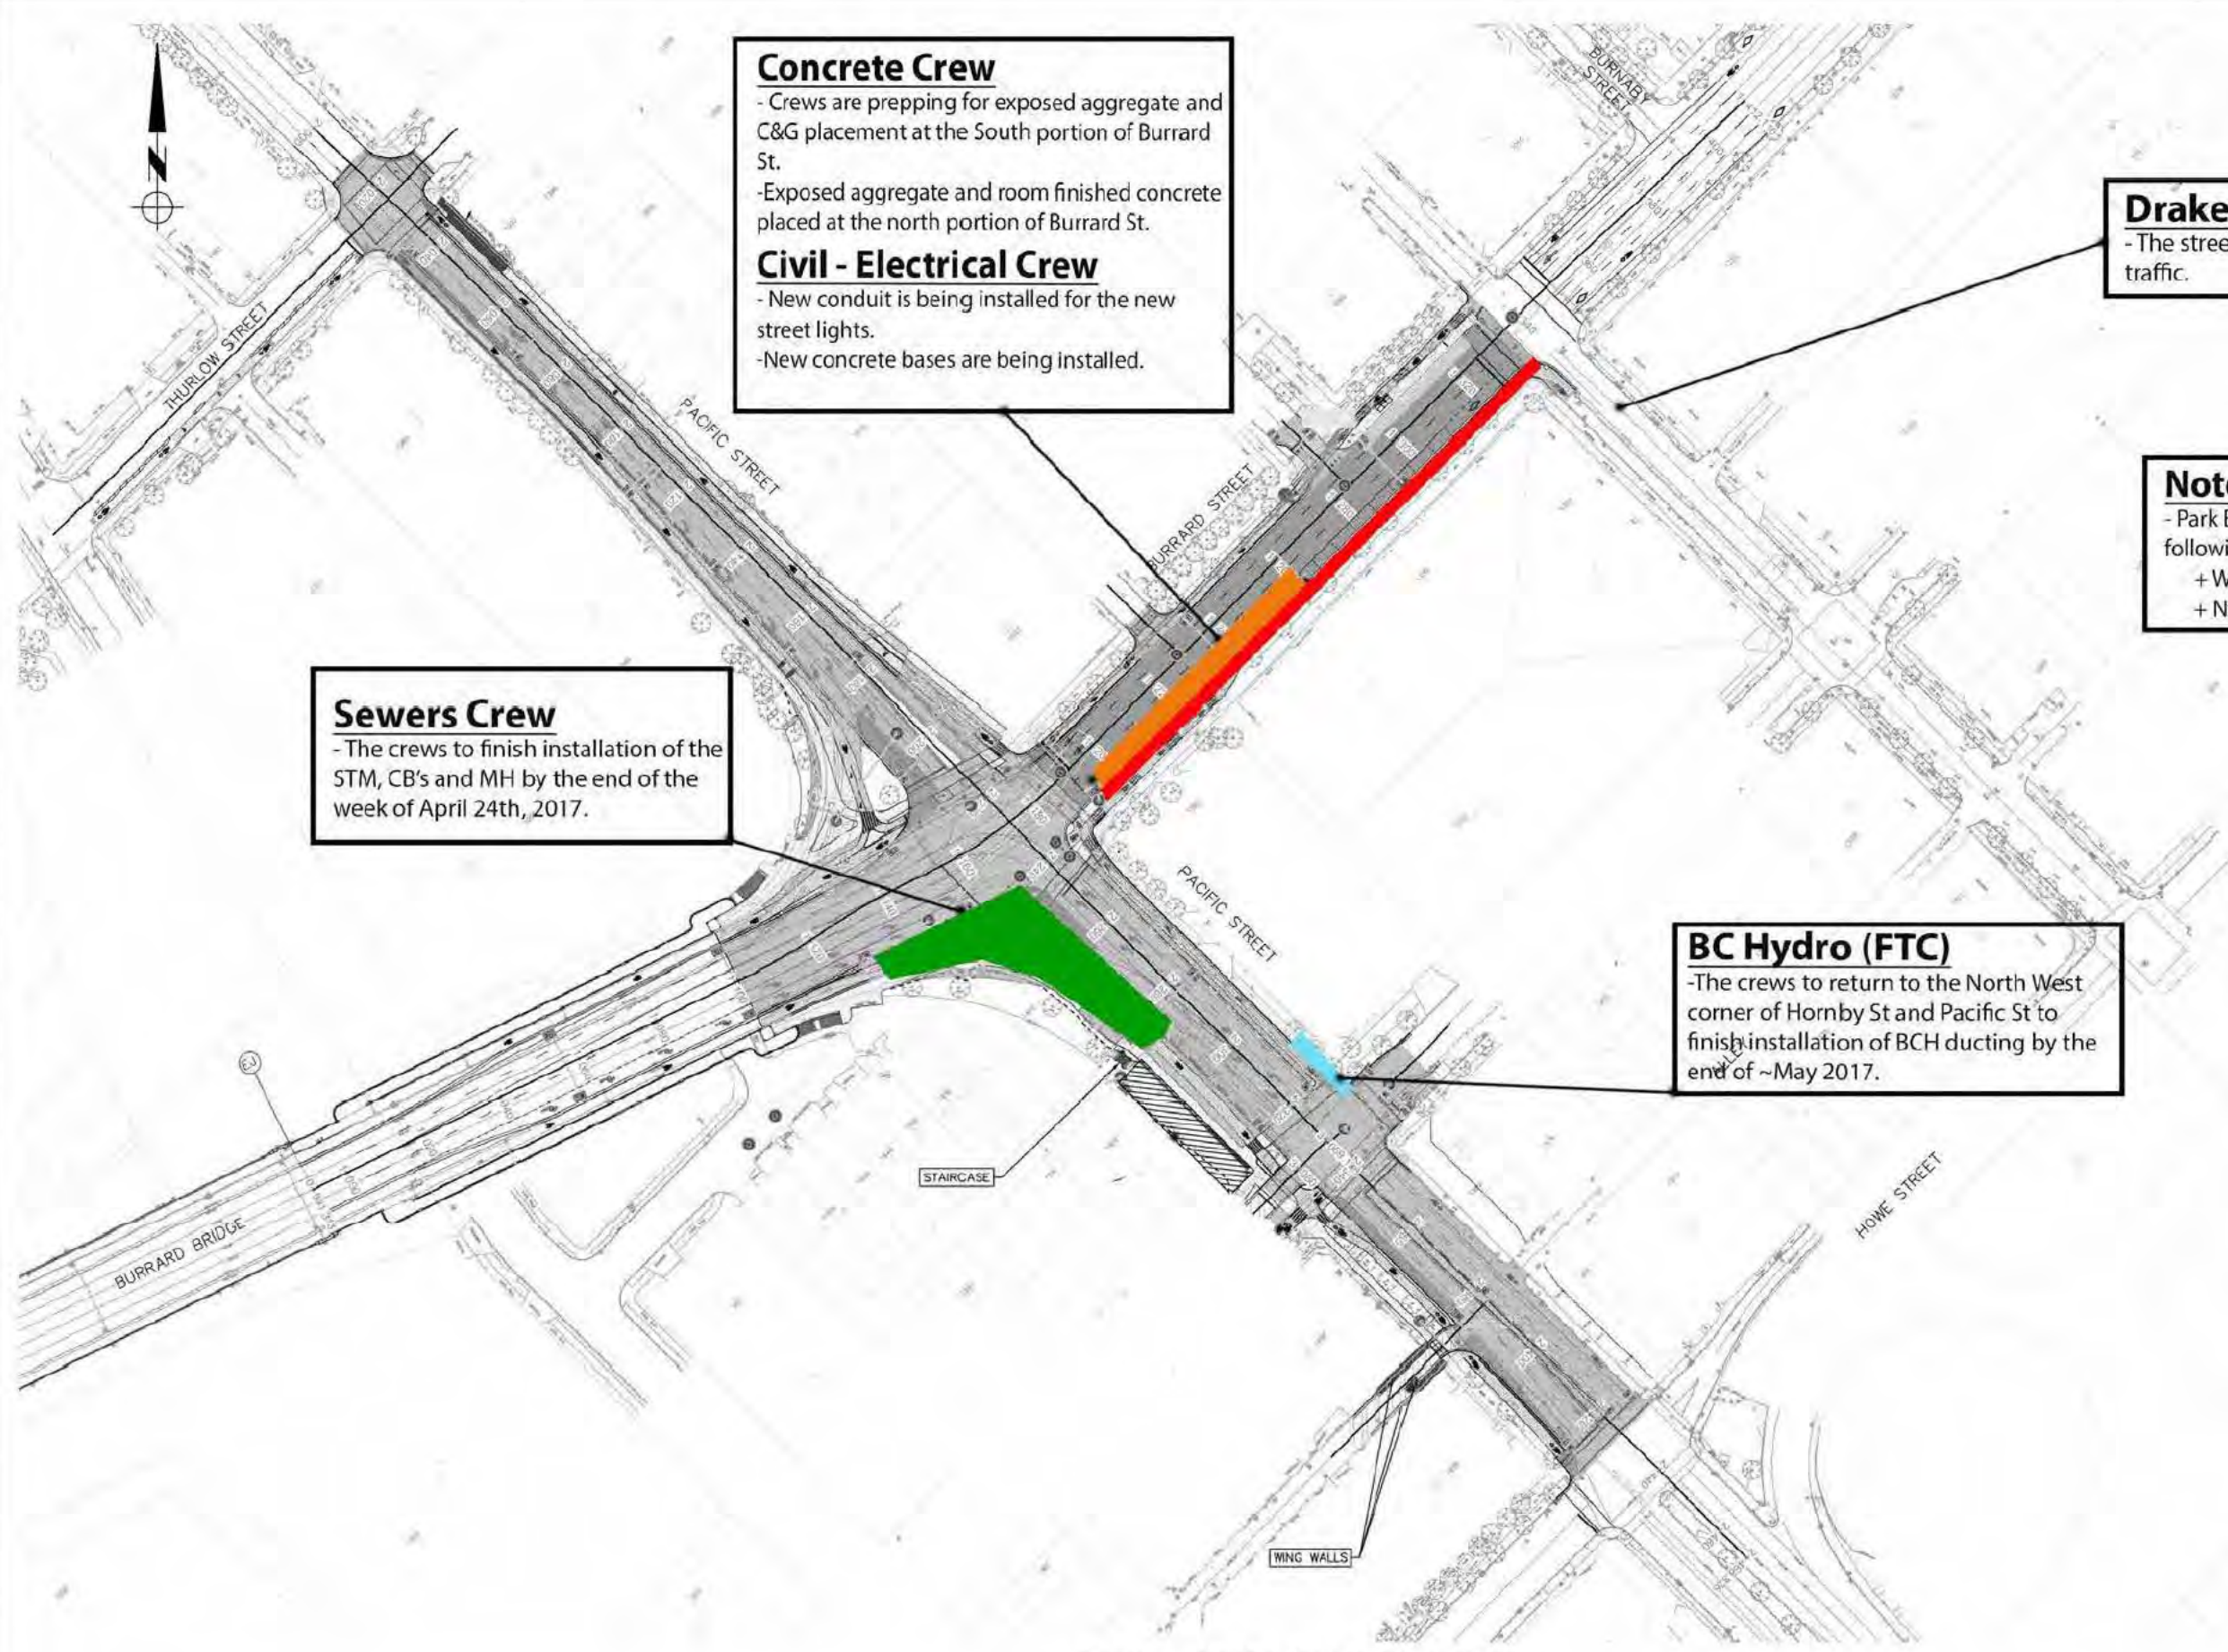

PLAN – SCOPE OF MAJOR WORKS
SCALE: 1:750

From: "Currie, David" <David.Currie@vancouver.ca>
To: "Currie, David" <David.Currie@vancouver.ca>
Date: 4/20/2017 1:38:25 PM
Subject: Fwd: BURRARD NORTH DAILY TMP REPORT - April 20
Attachments: image1.jpeg
image2.jpeg
image3.jpeg
image4.jpeg
image5.jpeg
image6.jpeg
image7.jpeg
image8.jpeg
image9.jpeg
image10.jpeg

Dave Currie, P.Eng.
Senior Project Manager
Burrard Bridge North Project
Engineering Services
City of Vancouver
T. 604-871-6656
C.604-679-1200

Begin forwarded message:

From: Marion <mdegear@telus.net>
Date: April 20, 2017 at 1:09:12 PM PDT
To: Sherwood Plant <Sherwood.Plant@vancouver.ca>, Greg Nowak
<Greg.Nowak@vancouver.ca>
Cc: David Currie <David.Currie@vancouver.ca>, Raul Armendariz
<raul.armendariz@vancouver.ca>, Sarah Wilson <Sarah.Wilson@vancouver.ca>,
Jack Durnford <Jack.Durnford@vancouver.ca>, Jasvinder Hothi
<Jasvinder.Hothi@vancouver.ca>
Subject: BURRARD NORTH DAILY TMP REPORT - April 20

Good afternoon everyone,

Ansan (Marion DeGear) reviewed the Burrard & Pacific base TMP and noted all signs and markings were in the correct position at the start of the day.

I am however noticing the centreline on the bridge (Grahams) northbound, the 2-way arrows stop just before the crest of the bridge. With the next 2-way being at the intersection of Pacific & Burrard.



BURRARD - PACIFIC SE CORNER

Ansan (Marion DeGear) reviewed the days scope of work with sewer foreman (Tito) TCP's (Tracey & Kerry). It was discussed vector on site for M/H excavation. Excavations continue, Sea to Sky pick up sheet shoring & lumber.



Pacific base TMP was modified as follows:

- Pacific traffic is in a counterflow diversion in the westbound lanes from west of Burrard too east of Hornby.
- East bound bridge off ramp traffic has been diverted NW of the Construction site.
- Bike detour installed (own bike lane) along side of traffic.

-cyclist & Pedestrians share a partial part of the sidewalk on the SW corner.

BURRARD EAST SIDE - NORTH END

Ansan (Marion DeGear) reviewed today's scope of work with Streets concrete crew Forman (Marijan), it was discussed material will be added to trench. Jack hammering out a couple of old bases & curb.



BURRARD - WESTSIDE SIDEWALK (Between Harwood & Drake)

Ansan (Marion DeGear) discussed with Parks Dept. Forman (Fraser) were on site to plant 4 trees on Burrard Street & 3 on the NW corner of Burrard & Pacific. Parks has now demobilized.



If you have any questions please call.

Thank you,

Marion DeGear
ANSAN - LCS
C# 604.306.0085

Sent from my iPhone











