

From: ["EOC Planning Chief \Vancouver\"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/19/2022 6:06:57 PM
Subject: Sit Rep - EOC Hasting Destructuring - Aug 19/2022
Attachments: 2022-08-19- Situation Report - Hastings Destructuring.pdf

Hi all,

\~

Please see attached for the EOC Sit Rep for today, August 19, 2022.

\~

Best,
Gillian

\~

Gillian Wong

Deputy Planning Chief
Emergency Operations Centre
City of Vancouver

E s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 19, 2022
Time	18:00
Operational Period	1 (Aug 16-19)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Gillian Wong, Deputy Planning Chief
Authorized by	Daniel Stevens, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO**Email:** s.15(1)(l)

1. EOC Update
 - a. Small core staff for the weekend
 - Small contingent of EOC management team
 - Field staff and logistics support
 - Phase 3 planning
 - Situation reporting
 - EOC workspace setup – 6th floor
 - b. Challenge: Staff availability for EOC roles, particularly leadership and planning
2. Action Plan for operational period #2 (Mon 22 – Sun 28) drafted – finalized tomorrow
3. EOC safety team on site today
4. Phase 1 operations will continue. Next decision point is Sept 6th.

Summary: Status & Risks

Overview of all EOC objectives for operational period #1

#	EOC Objective	Status/Target	Risks/Issues/Decisions
1	De-Structuring operations	In progress	
2	Community Supports		
	a. Automated public toilet	August 25	
	b. Mobile washroom trailer	August 22	
	c. Storage: Short term	August 18	
	d. Storage: Long term	August 19	
	c. Housing	In progress	
3	Communications	In progress	
4	Monitoring Parks	In progress	s.13(1)

Status Legend:

Not started

In progress

Complete

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

Overview of all EOC objectives for operational period #1

#	EOC Objective	Status/Target	Risks/Issues/Decisions
5	Phase 3 Planning	August 19	s.13(1)
6	Impoundment Plan	In progress	
7	Establish EOC	August 19	Issue (1): Staff availability for the EOC is not meeting EOC staffing needs
8	Track and forecast costs	In Progress	

Status Legend:

Not started

In progress

Complete

On hold/ Issues

Cancelled

Overview of key metrics that inform phase 2

		Aug 17	Aug 18	Aug 19	TOTAL
1	# of priority sites cleared (X/10)	2	2.5	0	4.5
2	# fire department connections made accessible	1	2	0	3
3	# of structures taken down	3	3	2	8
4	# new structures have appeared between Abbott & Gore	1	3	1	5
5	# new structures have appeared in DTES parks	14	15	10	39
6	# of new people that are sheltering in DTES parks	20	20	12	52
	a. Andy Livingstone	5	-	2	-
	b. CRAB	9	-	5	-
	c. Oppenheimer	2	-	3	-
	d. Strathcona	2	-	1	-
	e. McLean	0	-	0	-
	f. Pigeon	2	-	1	-

Overview of key metrics that inform phase 2

		Aug 17	Aug 18	Aug 19	TOTAL
7	# unhoused people within Abbott to Gore that have been offered shelter or housing (of approximately 210 people)	0	0	0	0
8	# of shelter spaces available today	10	17	14	-
9	# of SRO units ready for tenanting today	30	30	30	-
10	Estimated # of SRO units available by end of next week	N/A	N/A	20	-

- Heat Warning was rescinded today
- External partners will be provided weekly updates (Mondays)

Reporting by EOC Objective

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Remove priority structures from sidewalks along Hastings Street

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Remove structures that are impeding fire department connections & building entrances & exits	In progress		OPS – ENG
2	Remove priority structures at Regent Hotel & 12 E Hastings	In progress		OPS – ENG
3	Continue removing structures and material to reduce fire risk, fuel load and congestion on Hastings between Abbott and Gore	In progress		OPS – ENG

Comments

- None

In addition to key metrics provided on pages 3-4, the following metrics are being tracked.

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	Tonnage of material removed	4500kg	3500kg	
2	# of propane tanks removed	4	2	
3	# of tents taken down	3	2	
4	# of carts distributed by Sanitation	20	20	
5	# of staffing resources deployed by ENG	18	18	
6	# of staffing resources deployed by Carnegie Outreach	2	2	

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Install and operationalize a peer supported APT in Pigeon Park

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Schedule installation of APT.	Aug 25		OPS – ENG
2	Resolve staffing and security issues related to installation.	Aug 18		OPS – ENG
3	Resolve interim workplace supports for peer operators.	Aug 18		OPS – ENG

Comments

- Installation will be complete Aug 22 and the toilets will be operational by Aug 25.
- Outfront has numbers for OPS to support on site and Sanitation will provide employee. OPS and Sanitation will be on site on Monday.
- Table, chairs and Tent will be used until Britco trailer delivered.

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Deploy and operationalize a peer supported mobile washroom trailer at Columbia and Hastings St.

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Execute an extended service agreement with SuperSave.	August 17		OPS – ACCS
2	Take possession of the trailer and develop deployment plan for daily delivery servicing and removal.	August 19		OPS – ENG
3	Secure street use permits for replacement of trailer.	August 19		OPS – ENG
4	Coordinate power to the trailer.	August 19		OPS – ACCS

Comments

- s.13(1) [REDACTED]
- Sanitation has agreed to assist with daily deployment and McRae's will do daily emptying and filling of water.
- Meeting with REFM Electrical tomorrow onsite to figure out power source and how to do this. Need to confirm BC Housing is ok with us using their building to draw power from.

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop and implement short term storage solutions at 390 Main Street

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Fully execute operator contract with Aboriginal Front Door Society and confirm hours of operation (Hours have been 12-16)	August 17	Contract being elevated by EOC. Hours have been 12-16 but no confirmation on time/hours yet.	OPS – ACCS
2	Streamline process of transporting packed belongings to storage via Clean Start.	August 18		OPS – ACCS

Metrics

#	Metric	Aug 18	Aug 19	Aug 20
1	# of totes at 390 Main	4	1 (6 people total; 8 totes total)	
2	Status of capacity at Main (% full; out of 73)	5.5%	35%	

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop and implement long term storage solutions at 987 E. Cordova

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Identify and confirm third party operator to manage movement of items in and out of storage.	August 19		OPS – ACCS
2	Develop storage agreement form to be completed by people storing items in long term storage.	Cancelled		OPS – ACCS
3	Develop process for how individuals get connected with storage operators, register for storage services and transition their belongings in and out of storage.	Cancelled		OPS – ACCS

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	# of totes at 987 E. Cordova	0	0	
2	Status of capacity at Cordova (% full; out of 24)	0	0	
3	# of totes at Atira Women's Storage (101 E. Cordova)	7	10	
4	Status of capacity at Atira (% full; out of 20)	35%	50%	

Comments

- Meeting with CleanStart on Aug 22 regarding extending current contract

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Enhance external communication to media, public and people sheltering outdoors

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop overall communications plan for Phase 1 operations.	In progress		Information officer
2	Develop key messages for media to support Phase 1.	Complete		Information officer
3	Develop key messaging and communication products (e.g. flyers, posters) for people sheltering outdoors for Phase 1.	In progress		Information officer
4	Develop communication strategy in alignment with VPD and VFRS to support Phase 2 operations.	In progress		Information officer

Comments

- None

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	# of media requests received and responded^	0	-	
2	# of flyers distributed	50	0	

^Media numbers are available the following day

Status Legend:	Not started	In progress	Complete	On hold/ Issues	Cancelled
----------------	-------------	-------------	----------	-----------------	-----------

Objective: Enhance external communication to media, public and people sheltering outdoors

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop messaging to connected leaders and all staff regarding activation of EOC	Complete		Information officer
2	Develop GM messaging to ACCS and Engineering department staff.	Complete		Information officer

Comments

- None

Downstream impacts in Parks

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Monitor downstream impacts in CoV Parks

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Monitor the number of daily structures appearing in CoV parks and track which structures are directly related to people who were sheltering outdoors on Hastings Street.	In progress	s.13(1)	OPS – Park Board

Comments

- The other parks checked today did not have any new tents or individuals

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop long term sustainment strategy for management of Hastings Street (Phase 3)

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop Phase 3 sustainment plan	August 24	s.13(1)	Planning
2	Identify funding sources to support sustainment plan.	August 24		Planning
3	Develop resourcing plan to support sustainment plan.	August 22	Risk (1): Issues hiring staff	Planning

Comments

- Framework developed; will inform development of Phase 3 Operational Plan for Period 2.

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop impoundment plan for seized materials

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Identify locations to store impounded materials.	Complete		OPS - ENG
2	Develop cataloguing and inventory system for impounded materials.	Complete		OPS - ENG
3	Develop repatriation process to enable people to reclaim impounded items.	In progress		OPS - ENG
4	Develop public facing messaging to support the plan.	In progress		Information Officer

Comments

- Plan document is 95% complete
- Outstanding items are related to finalizing details in the repatriation process (all are in-progress):
- Document that will be given to citizens whose items are impounded that describes how to get their items back
- 311 scripting for receiving requests to claim impounded items (working with 311)
- Finalizing the pre-determined drop-off location (working with ACCS)
- Plan to focus upcoming flyers on voluntary storage options given the extension of Phase 1. Will continue to assess the need for adding this language.
- Looking at additional storage locations in the DTES next week which could be used as an alternate to National Yards and make repatriation easier for citizens.

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Establish EOC

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	Develop staffing schedule to Sept 20th, fill shifts for initial two weeks.	Ongoing	Issue (1): Staff availability for EOC is not currently meeting EOC staffing needs.	Planning
2	Develop and distribute EOC Org chart.	Complete		Planning
3	Add EOC and other incident staff to appropriate DLs for Teams/SharePoint access.	Ongoing		Planning

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop initial financial forecast

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	Draft initial forecast by Thursday.	Complete		Finance

Comments

- The first draft financial costing and forecast is complete – we will continue to update costs and forecasts on a weekly basis

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
2	# of Evelyn Saller meal tickets distributed by ENG teams	10	0	
3	Incremental public safety stats (TBC)	--	--	

Comments

- Funding for meals provided through Better Life Foundation ended on August 15th. No more meals being distributed unless new funding is secured.

End of document

From: ["Clark, Elizabeth" <Elizabeth.Clark@vancouver.ca>](mailto:Elizabeth.Clark@vancouver.ca)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/20/2022 4:19:33 PM
Subject: Sit Rep - EOC Hasting Destructuring - Aug 20/2022
Attachments: 2022-08-20- Situation Report - Hastings Destructuring (1).pdf

Hello all,

\~

Please see the attached EOC Situation Report for Today, August 18, 2022.

\~

Note that this Sit Rep had been updated to reflect the objectives and tasks outlined in EOC Action Plan #2. Updates on some objectives will be minimal today and tomorrow given the nature of weekend operations.

\~

Best,

Elizabeth

\~

Elizabeth Clark | EOC Planning Chief

City of Vancouver Emergency Operations Centre

s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 20, 2022
Time	16:00
Operational Period	2 (Aug 20-26)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Elizabeth Clark, Planning Chief
Authorized by	Daniel Stevens, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO**Email:** s.15(1)(l)

1. Slow but continued progress today.
2. Additional tents are appearing in parks around the city but it is not clear that these are directly related to destructuring on East Hastings.
3. Development of a business case to support Phase 3 planning continues.
4. BC Housing has confirmed that Extreme Weather Response shelters can activate early (October 15) to bring additional capacity online sooner than would normally be available.
5. Counsellors will be available at EOC and during scheduled drop in times at DTES community centres seven days a week going forward.
6. EOC Operations
 - a. Operational period #2 has commenced as of today and will run through Friday, August 26.
 - b. Action Plan #2 (Sat. Aug. 20 – Fri. Aug. 26) distributed today.

1. Press conference scheduled for 10am on Wednesday August 24th for CoV, VFRS and BC Housing.
2. ECCC has advised that a heat warning may be possible, although not certain, starting Wednesday, Aug 24th.

Summary: Status & Risks

Overview of all EOC objectives for operational period #2

#	EOC Objective	Status/Target	Risks/Issues/Decisions
1	De-Structuring operations	In progress	s.13(1)
2	Community supports		
	a. Automated public toilet	August 26	
	b. Mobile washroom trailer	August 25	
	c. Storage	August 22	
	d. Housing	In progress	
3	Communications	In progress	
4	Monitoring Parks	In progress	
5	Phase 3 planning	August 24	
6	Impoundment plan	August 26	
7	Enhance EOC operations	August 26	
8	Track and forecast costs	In Progress	

Status Legend:

Not started

In progress

Complete

On hold/ Issues

Cancelled

Overview of all EOC objectives for operational period #2

#	EOC Objective	Status/Target	Risks/Issues/Decisions
6	Occupational health and safety	August 23	
7	Tracking support services	In Progress	
8	Coordination with partners	In Progress	

Status Legend:

Not started

In progress

Complete

On hold/ Issues

Cancelled

Overview of key metrics that inform phase 2

		Aug 17	Aug 18	Aug 19	Aug 20	TOTAL
1	# of priority sites cleared (X/10)	2	2.5	0	0	4.5
2	# fire department connections made accessible	1	2	0	1	4
3	# of structures taken down	3	3	2	2	10
4	# new structures have appeared between Abbott & Gore	1	3	1	3	8
5	# new structures have appeared in DTES parks	14	15	10	22	61
6	# of new people that are sheltering in DTES parks	20	20	12	29	81
	a. Andy Livingstone	5	-	2	-	-
	b. Crab	9	-	5	9	-
	c. Oppenheimer	2	-	3	5	-
	d. Strathcona	2	-	1	1	-
	e. McLean	0	-	0	-	-
	f. Pigeon	2	-	1	-	-
	g. Other (total)	-	-	5	14	19

Overview of key metrics that inform phase 2

		Aug 17	Aug 18	Aug 19	Aug 20	TOTAL
7	# unhoused people within Abbott to Gore that have accepted offer of housing (of approximately 210 people)	0	0	0	0	0
	# unhoused people within Abbott to Gore that have accepted offer of shelter (of approximately 210 people)	-	-	-	2	2
8	# of shelter spaces available today^	10	17	14	31	-
9	# of SRO units ready for tenanting today	30	30	30	20	-
10	Estimated # of SRO units available by end of next week	N/A	N/A	20	20	-

^20 additional shelter spaces added through BC Housing as of today

Reporting by EOC Objective

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Remove priority structures from sidewalks along Hastings Street

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Remove structures that are impeding fire department connections & building entrances & exits.	In progress		OPS – ENG
2	Remove priority structures at the Regent, 2 E Hastings, 15 E Hastings, 41 to 57 E Hastings, 123 E Hastings and 123 (½) E Hastings.	In progress		OPS – ENG
3	Continue removing structures and material to reduce fire risk, fuel load and congestion on Hastings between Abbott and Gore.	In progress		OPS – ENG
4	Accelerate the transition of packed items and totes into storage.	In progress		OPS – ACCS

In addition to key metrics provided on pages 3-4, the following metrics are being tracked.

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	Tonnage of material removed	4500kg	3500kg	3000kg
2	# of propane tanks removed	4	2	0
3	# of tents taken down	3	2	1
4	# of carts distributed by Sanitation	20	20	14
5	# of staffing resources deployed by ENG	18	18	12
6	# of staffing resources deployed by Carnegie Outreach	2	2	3

Comments

- No new locations cleared today but downsizing is ongoing.
- Fire connection at 6 E Hastings is in process of being cleared.
- People continue to be reluctant to place carts into storage.

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Install and operationalize a peer supported APT in Pigeon Park

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Schedule installation and operationalization of APT.	August 26		OPS – ENG
2	Coordinate and schedule installation and security plan for the peer kiosk (Britco)	Aug 26		OPS – ENG

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Deploy and operationalize a peer supported mobile washroom trailer at Gore and Hastings St.

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Execute an extended service agreement with washroom trailer vendor.	August 23		OPS – ACCS
2	Finalize deployment plan for daily delivery servicing and removal.	August 24		OPS – ENG
3	Secure street use permits for replacement of trailer.	August 24		OPS – ENG
4	Coordinate power to the trailer.	August 25		OPS – ACCS

Comments

- None

Status Legend:

Not started

In progress

Complete

On hold/ Issues

Cancelled

Objective: Support transition of packed totes into storage in collaboration with community partners

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Confirm whether AFDS requires any potential logistical support to transition packed totes into storage (l.e via additional community partner or other)	August 22		OPS – ACCS

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	# of totes at 390 Main	4	1 (6 people total; 8 totes total)	--
2	Status of capacity at Main (% full; out of 73)	5.5%	35%	--
3	# of totes at 987 E. Cordova	0	0	0
4	Status of capacity at Cordova (% full; out of 24)	0%	0%	0%
5	# of totes at Atira Women's Storage (101 E. Cordova)	7	10	--
6	Status of capacity at Atira (% full; out of 20)	35%	50%	--

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop impoundment plan for seized materials

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Finalize cataloguing and inventory system for impounded materials.	August 24		OPS - ENG
2	Finalize repatriation process to enable people to reclaim impounded items (inclusive of delivering items to identified housing or exchange locations).	August 26		OPS - ENG
3	Finalize public facing messaging to support the plan.	August 26		Information Officer

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Monitor downstream impacts in CoV Parks

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Monitor the number of daily structures appearing in CoV parks and track which structures are directly related to people who were sheltering outdoors on Hastings Street.	In progress		OPS – Park Board
2	Track structure related 311 complaints.	In progress		OPS – Park Board

Comments

- None

Tracking of Service Supports

Status Legend:	Not started	In progress	Complete	On hold/ Issues	Cancelled
----------------	-------------	-------------	----------	-----------------	-----------

Objective: Track service supports available to Hastings community members

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	Compile a list and track status of service supports available to Hastings community members and provide to provincial partners	August 22		Planning

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Enhance external communication to media, public and people sheltering outdoors

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop key messaging and communication products (e.g. flyers, posters) for people sheltering outdoors for Phase 1.	In progress		Information Officer
2	Finalize communication strategy in alignment with VPD and VFRS to support Phase 2 operations.	August 26		Information Officer
3	Coordinate media briefing for August 24 and develop associated media advisory and information bulletin.	August 24		Information Officer
4	Work with VCH and BC Housing to align messaging for Aug. 24 media briefing and ongoing public messaging.	August 20		Information Officer

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
1	# of media requests received and responded^	0	--	--
2	# of flyers distributed	50	0	--

Comments

- None

^Media numbers are available the following day

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop internal communications to staff

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop and communicate staff support available to ACCS, Engineering, EOC and other supporting personnel.	August 24		Information Officer
2	Continue providing updates to Mayor and Council.	In progress		Information Officer

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Develop long term sustainment strategy for management of Hastings Street (Phase 3)

#	Related Tasks	Status & expected/ actual completion date	Risks/issues	Responsible
1	Develop resourcing plan.	August 22		Planning
2	Identify strategies to deter structures at high-risk infrastructure (e.g. decals, art).	August 22		Planning
	Identify funding sources to plan.	August 24		Planning
3	Draft §.13(1) [REDACTED]	August 24		Planning

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Enhance EOC operations

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	<small>s.15(1)(l)</small>	August 22		LOG – EOC Support
2	Recruit additional EOC staff and develop staffing schedule through mid September.	August 26		LOG – EOC Support
3	Develop and implement staff onboarding process.	August 26		LOG – EOC Support

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Ensure occupational health and safety plans, processes and orientations are implemented for EOC and field staff

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	Implement a team to support health, physical, psychosocial and safety for EOC, outreach and field staff.	August 23		Safety (OH&S)
2	Establish a safety plan and safety orientation for new EOC employees on site s.15(1)(l)	August 22		Safety (OH&S)
	Implement an on site first aid team.	August 22		LOG – EOC Support
	Support occupational health and safety plans and processes.	August 23		LOG – EOC Support

Comments

- None

Status Legend: Not started In progress Complete On hold/ Issues Cancelled

Objective: Continue financial tracking and forecasting

#	Related Tasks	Status & expected/actual completion date	Risks/issues	Responsible
1	Continue working the departments to track current and forecasted costs.	Ongoing		Finance

Comments

- None

Metrics				
#	Metric	Aug 18	Aug 19	Aug 20
2	# of Evelyn Saller meal tickets distributed by ENG teams	10	0	0
3	Incremental public safety stats (TBC)	--	--	--

Comments

- None

End of document

From: ["EOC Planning Chief \ \(Vancouver\)"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/23/2022 6:01:05 PM
Subject: Sit Rep - EOC Hastings Destructuring - Aug 23/2022
Attachments: 2022-08-23- Situation Report - Hastings Destructuring.pdf

Hello all,

\~

Please see the attached EOC Situation Report for today, August 23, 2022.

\~

Full updates on all tasks from the action plan will be distributed on Thursday.

\~

Best,

\~

Gillian Wong

Deputy Planning Chief

Emergency Operations Centre

City of Vancouver

E s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 23, 2022
Time	18:00
Operational Period	2 (Aug 20-26)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Gillian Wong, Deputy Planning Chief
Authorized by	Branislav Henselmann, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO**Email:** s.15(1)(l)

1. Fire at 568 Powell Street and 215 Princess St.
 - Neither site will be reoccupied without significant remediation so residents are displaced indefinitely.
 - Emergency Support Services (ESS) continues to provide ongoing support to displaced residents.
A meeting for evacuees was held today and another is set for tomorrow.
2. First Responder meeting was productive. Open invitation for follow up meetings as needed.

1. Cheque Day is tomorrow, Aug 24
2. Press conference scheduled for 10am on Wednesday August 24th for CoV, VFRS, and BC Housing. CEC has received ~10 media RSVPs at time of reporting.
3. EOC continues to monitor potential for heat event this coming week. Latest information from Environment Canada forecasts that there will not be a heat warning and that air quality from wildfire smoke is not currently at dangerous levels.

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
1	Health and Safety	August 23	<ul style="list-style-type: none"> Counsellors support on-site weekdays
2	De-Structuring Operations	In progress	s.13(1)
3	Community Supports		
	a. Outreach Operations	Ongoing	<ul style="list-style-type: none"> Connecting people with supports and identify emerging issues.
	b. APT - Pigeon Park	Aug 25	<ul style="list-style-type: none"> Kiosk will be operational Sept 2. APT operation is not contingent on the kiosk being operational.
	c. Mobile Washroom Trailer - Gore & Hastings	Delayed: Aug 31	s.13(1)
	d. Comfort Stations	Ongoing	

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
	e. Storage & Drop in		
	- 390 Main (Storage and Drop in)	Ongoing	<ul style="list-style-type: none"> Aboriginal Front Door operational today. Hours from 10-2. Planning for drop in. Food program starting up.
	- 987 E Cordova (Storage)	Ongoing	<ul style="list-style-type: none"> No issues to report
	- 320 Alexander (Drop in only)	In progress	s.13(1)
	- 101 Cordova St (Women's Only storage)	Ongoing	<ul style="list-style-type: none"> The space opened on August 17th. Women are using storage. Hours are M-Fr 8:30-10:30 AM for drop off and 4-6 pick up 7 days per week.
	f. Housing and Shelters	In progress	s.13(1)
	g. Supports for Indigenous Peoples	Ongoing	<ul style="list-style-type: none"> Aboriginal Front Door began outreach today
	h. Supports for women	Ongoing	<ul style="list-style-type: none"> Still seeking space. Storage for women is available but drop in space not available.
4	Communications	Ongoing	<ul style="list-style-type: none"> Advisory issued for the media briefing on Aug 23 with City, VFRS and BCH. ~10 media RSVPs to date

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
5	Monitoring Parks	Ongoing	<div>s.13(1)</div>
6	Phase 3 Planning	August 24	
7	Coordination with Partners	Ongoing	
8	Impoundment Plan	August 26	

Status Legend:	Not started	In progress	Complete/ Ongoing	On hold/ Issues	Cancelled
----------------	-------------	-------------	-------------------	-----------------	-----------

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
9	Enhance EOC Operations	August 26	s.13(1)
10	Track and forecast costs	Ongoing	<ul style="list-style-type: none"> No identified issues

Status Legend:

Not started

In progress


Complete/ Ongoing

On hold/ Issues

Cancelled

De-construction

- 1** # of priority sites cleared /10
- 1** # Fire Department Connections made accessible
- 1** # of structures taken down
- 0** # new structures have appeared between Abbott and Gore

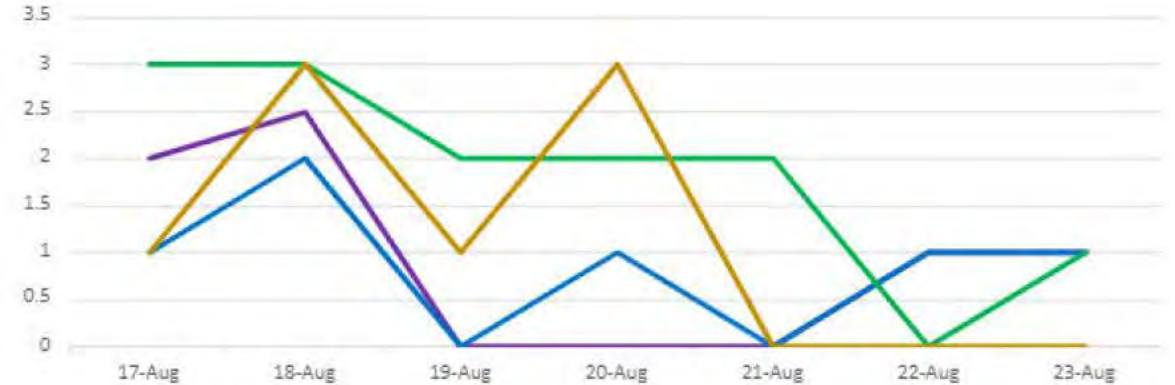

Housing & Shelters

- 0** # unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)
- 0** # unhoused people within Abbott - Gore that accepted offer of housing (~210 people)
- 31** # of shelter spaces available today
- 30** # of SRO units ready for tenanting today
- 20** Estimated # of SRO units available by end of next week

Monitoring Parks

	Structures	People
Total New	19	25
Andy Livingstone Park	4	6
Crab Park	8	10
Oppenheimer Park	2	2
Strathcona Park	1	2
McLean Park	1	1
Pigeon Park	1	1
Other Parks	2	3

De-construction

Required Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	Total (Since Aug 17)
# of priority sites cleared /10	2	2.5	0	0	0	1	1	6.5
# Fire Department Connections made accessible	1	2	0	1	0	1	1	6
# of structures taken down	3	3	2	2	2	0	1	13
# new structures have appeared between Abbott and Gore	1	3	1	3	0	0	0	8
# of tents taken down	--	3	2	1	2	2	3	13
# of carts distributed by Sanitation	15	20	20	14	3	4	0	76
# propane tanks removed	2	2	2	0	0	2	0	8
# flyers distributed	50	0	0	0	0	0	0	50
# of Evelyn Saller meal tickets distributed by ENG teams	25	10	0	0	0	0	45	80
Tonnage of material removed (kg)	2500	4500	3500	3000	2500	3000	2500	n/a
# of Operations Workers deployed	20	18	18	12	12	18	17	n/a
# of Supervisors deployed	3	--	2	1	1	2	2	n/a
# of Managers deployed	1	--	1	1	1	1	1	n/a
# of VFRS Inspectors deployed	4	4	4	2	2	3	4	n/a

Storage & Drop-ins

Required Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	Total (Since Aug 17)
# of staffing resources deployed @ Carnegie Outreach	2	2	2	3	3	3	2	n/a
# of totes @ 390 Main (73 tote capacity)	3	4	1	--	0	1	1	10
# of people storing totes @ 390 Main (73 tote capacity)	--	3	1	--	0	1	1	8
# of totes @ 987 E. Cordova (24 tote capacity)	0	0	0	0	0	0	0	n/a
# of people storing totes @ 987 E. Cordova (24 tote capacity)	--	--	0	0	0	0	0	n/a
# of totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	7	10	--	--	--	10	n/a
# of people storing totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	n/a

Housing & Shelters

Required Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	Total (Since Aug 17)
# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)	0	0	0	2	0	0	0	2
# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)	--	--	--	0	0	0	0	0
# of shelter spaces available today	10	17	14	31	33	35	31	n/a
# of SRO units ready for tenanting today	30	30	30	30	30	30	30	n/a
Estimated # of SRO units available by end of next week	--	--	20	20	20	20	20	n/a

Communications

Required Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	Total (Since Aug 17)
# of media requests received and responded *	0	0	0	0	1	1	--	2

* Reporting is 1 day delayed

Monitoring Parks

	17-Aug		18-Aug		19-Aug		20-Aug		21-Aug		22-Aug		23-Aug		Total (Since Aug 17)	
Metric	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People
Total New sheltering in DTES Parks	14	20	15	20	10	12	22	29	12	14	14	18	19	25	106	138
# New sheltering Andy Livingstone Park	2	5	2	--	1	2	--	--	2	3	1	2	4	6	--	--
# New sheltering Crab Park	7	9	4	--	5	5	--	9	2	3	4	6	8	10	--	--
# New sheltering Oppenheimer Park	2	2	3	--	2	3	--	5	2	3	2	2	2	2	--	--
# New sheltering Strathcona Park	2	2	3	--	1	1	--	1	2	2	1	2	1	2	--	--
# New sheltering McLean Park	0	0	2	--	0	0	--	--	2	2	1	1	1	1	--	--
# New sheltering Pigeon Park	1	2	1	--	1	1	--	--	1	--	1	0	1	1	--	--
# New sheltering at other parks	--	--	--	--	--	--	--	--	1	1	4	5	2	3	--	--

End of document

From: ["EOC Planning Chief \ \(Vancouver\)"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/24/2022 5:55:32 PM
Subject: Sit Rep - EOC Hastings Destructuring - Aug 24/2022
Attachments: 2022-08-24- Situation Report - Hastings Destructuring (1).pdf

Hello all,

\~

Please see the attached EOC Situation Report for today, August 24, 2022.

\~

A full update on all tasks from the EOC Action Plan will be distributed tomorrow (Thursday).

\~

Best,

Elizabeth

\~

Elizabeth Clark | EOC Planning Chief

City of Vancouver Emergency Operations Centre

s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 24, 2022
Time	17:50
Operational Period	2 (Aug 20-26)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Elizabeth Clark, Planning Chief
Authorized by	Daniel Stevens, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO**Email:** s.15(1)(l)

1. Steady progress continued today. Several locations outside of the ten priority fire locations were cleared and additional areas continue to be cleared.
2. Press conference was held today with broad coverage across media outlets.
3. Progress made regarding washroom trailer, APT and new potential storage space at 323 Alexander.
4. Key meetings with BC Housing occurred today.
5. Income and disability assistance payments were issued today (cheque day).
6. Fire at 568 Powell Street and 215 Princess Street
 - RainCity Housing, BC Housing and Emergency Support Services (ESS) continue to provide support to displaced individuals. s.22(1)
 - s.22(1)
 - Minimal impacts to sheltering options already committed to supporting Hastings operations.

1. Meeting with Veterans Manor is scheduled tomorrow to discuss using old Evelyn Saller site for women's drop-in.
2. EOC continues to monitor temperature and air quality levels. Environment Canada forecasts that there will not be a heat warning and that air quality from wildfire smoke is not currently at dangerous levels.

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
1	Health and Safety	August 23	<ul style="list-style-type: none"> Counsellors support on-site weekdays
2	De-Structuring Operations	In progress	s.13(1)
3	Community Supports		
	a. Outreach Operations	Ongoing	<ul style="list-style-type: none"> Was not in field today but will resume tomorrow (Aug 25). Connecting people with supports and identify emerging issues.
	b. Automated Public Toilet (APT) - Pigeon Park	Aug 25 (potential delay, will confirm tomorrow)	<ul style="list-style-type: none"> Crews onsite with Overdose Prevention Society (OPS) today for installation and testing. Kiosk will be operational Sept 2. APT operation is not contingent on the kiosk being operational.

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
	c. Mobile Washroom Trailer - Gore & Hastings	Delayed: Aug 31	s.13(1)
	d. Comfort Stations	Ongoing	
	e. Storage & Drop in		
	- 390 Main (Storage and Drop in)	Ongoing	• Aboriginal Front Door operational today. Hours from 10AM-2PM.
	- 987 E Cordova (Storage)	Ongoing	• No issues to report
	- 320 Alexander (Drop in only)	In progress	s.13(1)
	- 101 Cordova St (Women's Only storage)	Ongoing	• The space opened on August 17th. Women are using storage. Hours are M-Fr 8:30-10:30 AM for drop off and 4-6 pick up 7 days per week.

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	- 323 Alexander Street (Storage) - unconfirmed	Ongoing	<ul style="list-style-type: none"> Possible new storage location. Site visit conducted to assess as potential new storage space.
	f. Housing and Shelters	In progress	s.13(1)
	g. Supports for Indigenous Peoples	Ongoing	<ul style="list-style-type: none"> No issues identified.
	h. Supports for women	Ongoing	<ul style="list-style-type: none"> Still seeking space. Storage for women is available but drop in space not available.
4	Communications	Ongoing	<ul style="list-style-type: none"> Press conference with City, VFRS and BCH held today. No issues identified.
5	Monitoring Parks	Ongoing	s.13(1)

Status Legend:	Not started	In progress	Complete/ Ongoing	On hold/ Issues	Cancelled
----------------	-------------	-------------	-------------------	-----------------	-----------

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
6	Sustainment Planning (formerly Phase 3 Planning)	Ongoing	s.13(1)
7	Coordination with Partners	Ongoing	
8	Impoundment Plan	August 26	

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
9	Enhance EOC Operations	August 26	§.13(1)
10	Track and forecast costs	Ongoing	• No identified issues

Status Legend:

Not started

In progress


Complete/ Ongoing

On hold/ Issues

Cancelled

De-construction

For Aug 24	Total (Since Aug 17)	
0	6.5	# of priority sites cleared /10
9	15	# Fire Department Connections made accessible
0	13	# of structures taken down
0	8	# new structures have appeared between Abbott and Gore

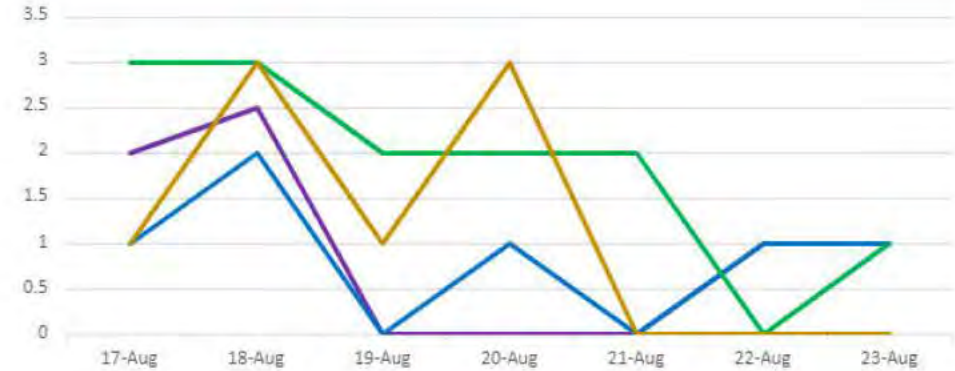

Housing & Shelters

For Aug 24	Total (Since Aug 17)	
0	2	# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)
0	0	# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)
35		# of shelter spaces available today
30		# of SRO units ready for tenanting today
20		Estimated # of SRO units available by end of next week

Communications

For Aug 23 *	Total (Since Aug 2)	
0	54	# of media requests received and responded to (previous day)

* Reporting is 1 day delayed

Monitoring Parks

	Total (Since Aug17)	
	Structures	People
Total New	118	155
	For Aug 24	
	Structures	People
Total New	12	17
Andy Livingstone Park	2	0
Crab Park	5	4
Oppenheimer Park	3	7
Strathcona Park	0	4
McLean Park	1	--
Pigeon Park	1	2
Other Parks	0	0

De-construction

Required Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	Total (Since Aug 17)
# of priority sites cleared /10	2	2.5	0	0	0	1	1	0	6.5
# Fire Department Connections made accessible	1	2	0	1	0	1	1	9	15
# of structures taken down	3	3	2	2	2	0	1	0	13
# new structures have appeared between Abbott and Gore	1	3	1	3	0	0	0	0	8
# of tents taken down		3	2	1	2	2	3	10	23
# of carts distributed by Sanitation	15	20	20	14	3	4	0	0	76
# propane tanks removed	2	2	2	0	0	2	0	3	11
# flyers distributed	50	0	0	0	0	0	0	0	50
# of Evelyne Saller meal tickets distributed by ENG teams	25	10	0	0	0	0	45	30	110
Tonnage of material removed (kg)	2500	4500	3500	3000	2500	3000	2500	2500	n/a
# of Operations Workers deployed	20	18	18	12	12	18	17	17	n/a
# of Supervisors deployed	3	--	2	1	1	2	2	3	n/a
# of Managers deployed	1	--	1	1	1	1	1	1	n/a
# of VFRS Inspectors deployed	4	4	4	2	2	3	4	2	n/a

Storage & Drop-ins

Storage & Drop-ins Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	Total (Since Aug 17)
# of staffing resources deployed @ Carnegie Outreach	2	2	2	3	3	3	2	0	n/a
# of totes @ 390 Main (73 tote capacity)	3	4	1	--	0	1	1	10	n/a
# of people storing totes @ 390 Main (73 tote capacity)	--	3	1	--	0	1	1	8	n/a
# of totes @ 987 E. Cordova (24 tote capacity)	0	0	0	0	0	0	0	--	n/a
# of people storing totes @ 987 E. Cordova (24 tote capacity)	--	--	0	0	0	0	0	--	n/a
# of totes @ 101 E. Cordova- Atira Women's Storage (20 tote capacity)	--	7	10	--	--	--	10	10	n/a
# of people storing totes @ 101 E. Cordova- Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	--	n/a

Housing & Shelters

Housing & Shelters Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	Total (Since Aug 17)
# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)	0	0	0	2	0	0	0	0	2
# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)	--	--	--	0	0	0	0	0	0
# of shelter spaces available today	10	17	14	31	33	35	31	35	n/a
# of SRO units ready for tenanting today	30	30	30	30	30	30	30	30	n/a
Estimated # of SRO units available by end of next week	--	--	20	20	20	20	20	20	n/a

Communications

Communications Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	Total (Since Aug 2)
# of media requests received and responded to (previous day) *	0	0	0	0	1	1	0		54

* Reporting is 1 day delayed

Monitoring Parks

	17-Aug		18-Aug		19-Aug		20-Aug		21-Aug		22-Aug		23-Aug		24-Aug		Total (Since Aug 17)	
Metric	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People
Total New sheltering in DTES Parks	14	20	15	20	10	12	22	29	12	14	14	18	19	25	12	17	118	155
# New sheltering Andy Livingstone Park	2	5	2	--	1	2	--	--	2	3	1	2	4	6	2	0	--	--
# New sheltering Crab Park	7	9	4	--	5	5	--	9	2	3	4	6	8	10	5	4	--	--
# New sheltering Oppenheimer Park	2	2	3	--	2	3	--	5	2	3	2	2	2	2	3	7	--	--
# New sheltering Strathcona Park	2	2	3	--	1	1	--	1	2	2	1	2	1	2	0	4	--	--
# New sheltering McLean Park	0	0	2	--	0	0	--	--	2	2	1	1	1	1	1	--	--	--
# New sheltering Pigeon Park	1	2	1	--	1	1	--	--	1		1	0	1	1	1	2	--	--
# New sheltering at other parks	0	0	0	0	0	0	0	0	1	1	4	5	2	3	0	0	--	--

End of document

From: ["EOC Planning Chief \Vancouver\"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/25/2022 7:03:15 PM
Subject: Sit Rep - EOC Hastings Destructuring - Aug 25/2022
Attachments: 2022-08-25- Situation Report - Hastings Destructuring.pdf

Hello all,

\~

Please see the attached EOC Situation Report for today, August 25, 2022, which includes updates on EOC objectives and tasks.

\~

Best,

\~

Gillian Wong

Deputy Planning Chief

Emergency Operations Centre

City of Vancouver

E s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 25, 2022
Time	19:00
Operational Period	2 (Aug 20-26)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Gillian Wong, EOC Deputy Planning Chief
Authorized by	Branislav Henselmann, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO

Email: §.15(1)(l)

1. The Veteran's Manor board is meeting today to discuss the use of old Evelyne Saller Centre (320 Alexander)
2. A second People and Support Services planning meeting with BC Housing took place today and will start including ministry partners and Indigenous housing partners next week.
3. Automated Public Toilet (APT) at Pigeon Park is planned to be activated tomorrow, Aug 25.
4. As of today, Emergency Support Services (ESS) is standing down services provided to residents displaced from 568 Powell Street and 215 Princess Street. RainCity Housing, BC Housing and the SRO operator of 215 Princess St. will continue to support evacuees and identify alternate housing solutions for residents.

1. Overdose Awareness Day is Wednesday, August 31. A march starting at VANDU to Main and Hastings as well as a block party are being planned and promoted via posters being circulated in the area.
2. Meeting with BIA is scheduled for tomorrow.
3. Temperatures will decrease as of tomorrow and remain in the low 20's through the weekend.
4. Tomorrow marks the end of Operational Period #2 (Aug 20-26) for the EOC. Action planning for Operational Period #3 (Aug 27-Aug 31) begins tomorrow morning. Note that operational periods #3 and #4 are shorter than previous operational periods s.13(1) [REDACTED]

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
1	Health and Safety	August 23	<ul style="list-style-type: none"> Counsellors support on-site weekdays Train-the-trainer sessions will be starting for staff
2	De-Structuring Operations	In progress	s.13(1)
3	Community Supports		
	a. Outreach Operations	Ongoing	<ul style="list-style-type: none"> No issues to report
	b. Automated Public Toilet (APT) - Pigeon Park	Aug 25 (potential delay, will confirm tomorrow)	s.13(1)

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	c. Mobile Washroom Trailer - Gore & Hastings	Delayed: Aug 31	s.13(1)
	d. Comfort Stations	Ongoing	
	e. Storage & Drop in		
	- 390 Main (Storage and Drop in)	Ongoing	• No issues to report
	- 987 E Cordova (Storage)	Ongoing	• No issues to report
	- 320 Alexander (Drop in only)	In progress	s.13(1)
	- 101 Cordova St (Women/ Gender Diverse Storage)	Ongoing	• No issues to report

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	- 323 Alexander Street (Storage) - unconfirmed	Ongoing	<ul style="list-style-type: none"> Possible new storage location. Site visit conducted to assess as potential new storage space.
	f. Housing and Shelters	In progress	s.13(1)
	g. Supports for Indigenous Peoples	Ongoing	<ul style="list-style-type: none"> No issues to report.
	h. Supports for women	Ongoing	<ul style="list-style-type: none"> No issues to report.
4	Communications	Ongoing	<ul style="list-style-type: none"> Updated Key Messages document Working on storage information flyers No risks or issues identified.
5	Monitoring Parks	Ongoing	s.13(1)

Status Legend:	Not started	In progress	Complete/ Ongoing	On hold/ Issues	Cancelled
----------------	-------------	-------------	-------------------	-----------------	-----------

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
6	Sustainment Planning (formerly Phase 3 Planning)	Ongoing	s.13(1)
7	Coordination with Partners	Ongoing	
8	Impoundment Plan	August 26	
9	Enhance EOC Operations	Complete/ August 26	
10	Track and forecast costs	Ongoing	• No identified issues

Status Legend:

Not started

In progress


Complete/ Ongoing

On hold/ Issues

Cancelled

De-construction

For Aug 25	Total (Since Aug 17)	
1	7.5	# of priority sites cleared /10
0	15	# Fire Department Connections made accessible
0	13	# of structures taken down
0	8	# new structures have appeared between Abbott and Gore

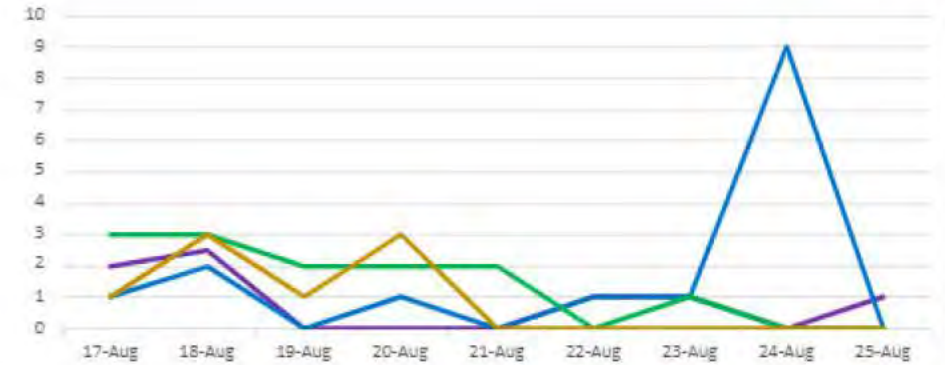

Housing & Shelters

For Aug 25	Total (Since Aug 17)	
0	2	# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)
0	0	# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)
41		# of shelter spaces available today
50		# of SRO units ready for tenanting today
0		Estimated # of SRO units available by end of next week

Communications

For Aug 24 *	Total (Since Aug 2)	
5	59	# of media requests received and responded to (previous day)

* Reporting is 1 day delayed

Monitoring Parks

		Total (Since Aug17)	
		Structures	People
Total New		134	177
		For Aug 25	
		Structures	People
Total New		16	22
Andy Livingstone Park		4	6
Crab Park		7	11
Oppenheimer Park		2	2
Strathcona Park		1	1
McLean Park		1	2
Pigeon Park		1	--
Other Parks		0	0

De-construction

De-construction Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	Total (Since Aug 17)
# of priority sites cleared /10	2	2.5	0	0	0	1	1	0	1	7.5
# Fire Department Connections made accessible	1	2	0	1	0	1	1	9	0	15
# of structures taken down	3	3	2	2	2	0	1	0	0	13
# new structures have appeared between Abbott and Gore	1	3	1	3	0	0	0	0	0	8
# of tents taken down		3	2	1	2	2	3	10	4	27
# of carts distributed by Sanitation	15	20	20	14	3	4	0	0	0	76
# propane tanks removed	2	2	2	0	0	2	0	3	0	11
# flyers distributed	50	0	0	0	0	0	0	0	0	50
# of Evelyn Saller meal tickets distributed by ENG teams	25	10	0	0	0	0	45	30	12	122
Tonnage of material removed (kg)	2500	4500	3500	3000	2500	3000	2500	2500	2500	n/a
# of Operations Workers deployed	20	18	18	12	12	18	17	17	16	n/a
# of Supervisors deployed	3	--	2	1	1	2	2	3	2	n/a
# of Managers deployed	1	--	1	1	1	1	1	1	1	n/a
# of VFRS Inspectors deployed	4	4	4	2	2	3	4	2	2	n/a

Storage & Drop-ins

Storage & Drop-ins Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	Total (Since Aug 17)
# of staffing resources deployed @ Carnegie Outreach	2	2	2	3	3	3	2	0	3	n/a
# of totes @ 390 Main (73 tote capacity)	3	4	1	--	0	1	1	10	10	n/a
# of people storing totes @ 390 Main (73 tote capacity)	--	3	1	--	0	1	1	8	8	n/a
# of totes @ 987 E. Cordova (24 tote capacity)	0	0	0	0	0	0	0	--	0	n/a
# of people storing totes @ 987 E. Cordova (24 tote capacity)	--	--	0	0	0	0	0	--	0	n/a
# of totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	7	10	--	--	--	10	10	10	n/a
# of people storing totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	--	--	n/a

Housing & Shelters

Housing & Shelters Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	Total (Since Aug 17)
# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)	0	0	0	2	0	0	0	0	0	2
# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)	--	--	--	0	0	0	0	0	0	0
# of shelter spaces available today	10	17	14	31	33	35	31	35	41	n/a
# of SRO units ready for tenanting today	30	30	30	30	30	30	30	30	50	n/a
Estimated # of SRO units available by end of next week	--	--	20	20	20	20	20	20	0	n/a

Communications

Communications Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	Total (Since Aug 2)
# of media requests received and responded to (previous day)	0	0	0	0	1	1	0	5		59

* Reporting is 1 day delayed

Monitoring Parks

	18-Aug		19-Aug		20-Aug		21-Aug		22-Aug		23-Aug		24-Aug		25-Aug		Total (Since Aug 17)	
Metric	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People
Total New sheltering in DTES Parks	15	20	10	12	22	29	12	14	14	18	19	25	12	17	16	22	134	177
# New sheltering Andy Livingstone Park	2	--	1	2	--	--	2	3	1	2	4	6	2	0	4	6	--	--
# New sheltering Crab Park	4	--	5	5	--	9	2	3	4	6	8	10	5	4	7	11	--	--
# New sheltering Oppenheimer Park	3	--	2	3	--	5	2	3	2	2	2	2	3	7	2	2	--	--
# New sheltering Strathcona Park	3	--	1	1	--	1	2	2	1	2	1	2	0	4	1	1	--	--
# New sheltering McLean Park	2	--	0	0	--	--	2	2	1	1	1	1	1	--	1	2	--	--
# New sheltering Pigeon Park	1	--	1	1	--	--	1		1	0	1	1	1	2	1	--	--	--
# New sheltering at other parks	0	0	0	0	0	0	1	1	4	5	2	3	0	0	0	0	--	--

Reporting by EOC Objective

EOC Objective

Ensure occupational health and safety plans, processes and orientations are implemented for EOC and field staff

#	Related Tasks	Status / Target	Risks / Issues
1	Implement a team to support health, physical, psychosocial and safety for EOC, outreach and field staff.	In progress/ Aug 23	
2	Establish a safety plan and safety orientation for new EOC employees on site s.15(1)(l)	In progress/ Aug 22	
3	Implement an on site first aid team.	In progress/ Aug 22	
4	Support occupational health and safety plans and processes.	In progress/ Aug 23	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Remove priority structures from sidewalks along Hastings Street

#	Related Tasks	Status / Target	Risks / Issues
1	Remove structures, prioritizing those that are impeding fire department connections and building entrances & exits.	Ongoing / Aug 26	Ongoing work on reducing the footprint of the existing structures, removing unwanted materials. Multiple tents were taken down. 9 Fire connections cleared, and one new entrance opened.
2	Remove priority structures at the following locations: Regent Hotel, 2-15 E. Hastings, 41-57 E. Hastings, 123 & 123 ½ E. Hastings	Ongoing / Aug 26	123 and 123 ½ cleared. Regent continuing to be reduced and more work on other areas.
3	Continue removing structures and material to reduce fire risk, fuel load and congestion on Hastings between Abbott and Gore.	Ongoing / Aug 26	Ongoing work on removing structures and combustible material.
4	Accelerate the transition of packed items and totes into storage.	Ongoing / Aug 26	Risk: slow movement of carts into storage. Some areas have accumulated multiple carts which are causing crowding issues on the street.

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Install and operationalize a peer supported APT in Pigeon Park

#	Related Tasks	Status / Target	Risks / Issues
1	Schedule installation and operationalization of APT.	Complete/ Aug 26	
2	Coordinate and schedule installation and security plan for the peer kiosk (Britco)	In progress/ Aug 26	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

APT is planned to be operational tomorrow, Aug 26.

EOC Objective

Deploy and operationalize a peer supported mobile washroom trailer at Gore and Hastings St.

#	Related Tasks	Status / Target	Risks / Issues
1	Execute an extended service agreement with washroom trailer vendor.	In progress/ Aug 23	
2	Finalize deployment plan for daily delivery servicing and removal.	In progress/ Aug 24	
3	Secure street use permits for replacement of trailer.	In progress/ Aug 24	
4	Coordinate power to the trailer.	In progress/ Aug 25	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Support transition of packed totes into storage in collaboration with community partners

#	Related Tasks	Status / Target	Risks / Issues
1	Confirm whether AFDS requires any potential logistical support to transition packed totes into storage (l.e via additional community partner or other)	In progress/ Aug 22	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Enhance external communication to media, public and people sheltering outdoors

#	Related Tasks	Status / Target	Risks / Issues
1	Develop key messaging and communication products (e.g. flyers, posters) for people sheltering outdoors for s.13(1)	In progress	
2	Finalize communication strategy in alignment with VPD and VFRS to support s.13(1) operations.	Aug 26	
3	Coordinate media briefing for August 24 and develop associated media advisory and information bulletin.	Complete	
4	Work with VCH and BC Housing to align messaging for Aug. 24 media briefing and ongoing public messaging.	Complete	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Develop internal communications to staff

#	Related Tasks	Status / Target	Risks / Issues
1	Develop and communicate staff support available to ACCS, Engineering, EOC and other supporting personnel.	Aug 24	
2	Continue providing updates to Mayor and Council.	In progress	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Monitor downstream impacts in CoV Parks

#	Related Tasks	Status / Target	Risks / Issues
1	Monitor the number of daily structures appearing in CoV parks and track which structures are directly related to people who were sheltering outdoors on Hastings Street.	In progress	
2	Track structure related 311 complaints.	In progress	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Develop long term sustainment strategy for management of Hastings Street (Phase 3)

#	Related Tasks	Status / Target	Risks / Issues
1	Develop resourcing plan.	Complete / Aug 22	
2	Identify strategies to deter structures at high-risk infrastructure (e.g. decals, art).	On hold/ Aug 22	Need new date
3	Identify funding sources to plan.	In progress / Aug 24	
4	Draft s.13(1), s.17(1)	New date: Aug 24	Resourcing plan needs to be approved first

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Track service supports available to Hastings community members

#	Related Tasks	Status / Target	Risks / Issues
1	Compile a list and track status of service supports available to Hastings community members and provide to provincial partners	Complete/ Aug 22	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Develop impoundment plan for seized materials

#	Related Tasks	Status / Target	Risks / Issues
1	Finalize cataloguing and inventory system for impounded materials.	Complete	
2	Finalize cataloguing and inventory system for impounded materials.	In Progress/ Aug 31	<ul style="list-style-type: none"> Outstanding item to get agreement on Pigeon Park as community pickup location. Target date moved out to allow for more urgent actions to be prioritized.
3	Finalize public facing messaging to support the plan.	In Progress/ Aug 31	<ul style="list-style-type: none"> Documents sent out for review. Target date moved out to allow for more urgent actions to be prioritized.

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Enhance EOC operations

#	Related Tasks	Status / Target	Risks / Issues
1	s.15(1)(l)	Complete/ Aug 22	
2	Recruit additional EOC staff and develop staffing schedule through mid-September.	Complete/ Aug 26	
3	Develop and implement staff onboarding process.	In progress/ Aug 26	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

EOC Objective

Continue financial tracking and forecasting

#	Related Tasks	Status / Target	Risks / Issues
1	Continue working with departments to track current and forecasted costs.	Ongoing	

Status Legend:

Not started

In progress

Complete

On hold / Issues

Cancelled

Comments

None.

End of document

From: ["EOC Planning Chief \Vancouver\"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 8/26/2022 6:10:24 PM
Subject: Sit Rep - EOC Hastings Destructuring - Aug 26/2022
Attachments: 2022-08-26- Situation Report - Hastings Destructuring.pdf

Hello all,

\~

Please see the attached EOC Situation Report for today, August 26, 2022.

\~

Best,

\~

Gillian Wong

Planning Chief

Emergency Operations Centre

City of Vancouver

E s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Aug 26, 2022
Time	18:00
Operational Period	2 (Aug 20-26)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Gillian Wong, EOC Deputy Planning Chief
Authorized by	Branislav Henselmann, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO	Email: s.15(1)(l)
-------------------------	--

1. The Automated Public Toilet (APT) at Pigeon Park is operational today
2. Meeting with BIA happened today and COV will be working with them on tailored communication planning moving forward.

1. Overdose Awareness Day is Wednesday, August 31. A march starting at VANDU to Main and Hastings as well as a block party are being planned and promoted via posters being circulated in the area.
2. Temperatures will remain in the low 20's today and through the weekend.
3. Today marks the end of Operational Period #2 (Aug 20-26) for the EOC. Operational Period #3 begins tomorrow, Aug 27.
4. The Action Plan for Operational Period #3 (Aug 27-Aug 31) is being reviewed and then will be distributed.

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments			
1	Health and Safety	In Progress/ August 29	<ul style="list-style-type: none">Safety orientation developed and will be delivered on an ongoing basis starting Aug 29thFirst aid and emergency plan completePsychological safety supports in place for EOC and field staffPhysical safety supports in place for EOC			
2	De-Structuring Operations	In progress	s.13(1)			
3	Community Supports					
	a. Outreach Operations	Ongoing	<ul style="list-style-type: none">No issues to report			
	b. Automated Public Toilet (APT) - Pigeon Park	Complete	<ul style="list-style-type: none">Operational as of today.Tasks related to operationalizing a kiosk are planned for Operational period #3.Currently activated and staffed until 9pm this evening. Fully operational from 9am – 9pm starting tomorrow.			
Status Legend:		Not started	In progress	Complete/ Ongoing	On hold/ Issues	Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	c. Mobile Washroom Trailer - Gore & Hastings	Delayed: Sep 15	s.13(1)
	d. Comfort Stations	Ongoing	
	e. Storage & Drop in		
	- 390 Main (Storage and Drop in)	Ongoing	• Open 7am-11pm starting Monday. Outreach on blocks of Hastings starting next week. Arranging meet and greet for Sanitation and AFDS outreach to develop process and protocol for next week.
	- 987 E Cordova (Storage)	Ongoing	• No issues to report
	- 320 Alexander (Drop in only)	In progress	s.13(1)
	- 101 E. Cordova St (Women/ Gender Diverse Storage)	Ongoing	• Met with Atira today to discuss improved operations plan and outreach alignment with Sanitation and Carnegie to improve uptake.

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	- 323 Alexander Street (Storage) - unconfirmed	Ongoing	<ul style="list-style-type: none"> Possible new storage location. Site visit conducted to assess as potential new storage space.
	f. Housing and Shelters	In progress	<ul style="list-style-type: none"> No issues to report.
	g. Supports for Indigenous Peoples	Ongoing	<ul style="list-style-type: none"> No issues to report.
	h. Supports for women	Ongoing	<ul style="list-style-type: none"> No issues to report.
4	Communications	Ongoing	<ul style="list-style-type: none"> No risks or issues identified.
5	Monitoring Parks	Ongoing	<p>s.13(1)</p>

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
6	Sustainment Planning (formerly Phase 3 Planning)	Ongoing	s.13(1)
7	Coordination with Partners	Ongoing	• No issues or risks to report.
8	Impoundment Plan	August 26	• No significant risks or issues. • Pre-impoundment and impoundment notices distributed for review.
9	Enhance EOC Operations	Complete	• No issues or risks to report.
10	Track and forecast costs	Ongoing	• No identified issues

Status Legend:

Not started

In progress


Complete/ Ongoing

On hold/ Issues

Cancelled

De-construction

For Aug 26	Total (Since Aug 17)	
0	7.5	# of priority sites cleared /10
All Clear	15	# Fire Department Connections made accessible
2	15	# of structures taken down
0	8	# new structures have appeared between Abbott and Gore

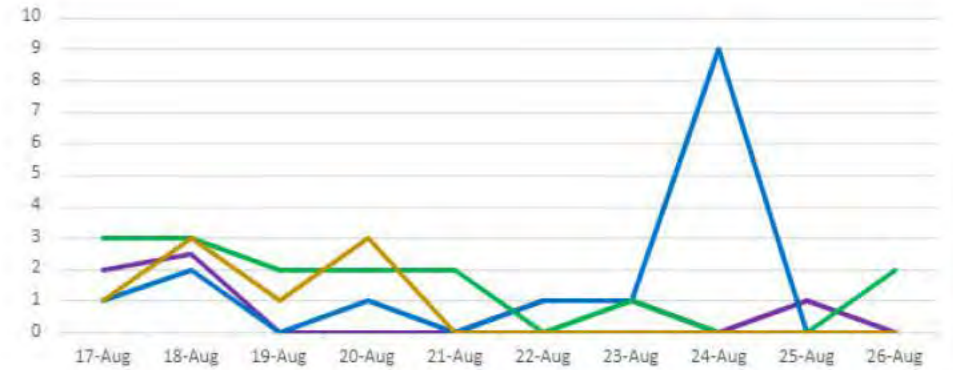

Housing & Shelters

For Aug 26	Total (Since Aug 17)	
1	3	# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)
0	0	# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)
37		# of shelter spaces available today
50		# of SRO units ready for tenanting today
2		Estimated # of SRO units available by end of next week

Communications

For Aug 25 *	Total (Since Aug 2)	
1	60	# of media requests received and responded to (previous day)

* Reporting is 1 day delayed

Monitoring Parks

	Total (Since Aug17)	
	Structures	People
Total New	147	197
	For Aug 26	
	Structures	People
Total New	13	20
Andy Livingstone Park	4	10
Crab Park	7	9
Oppenheimer Park	1	1
Strathcona Park	0	0
McLean Park	0	0
Pigeon Park	1	0
Other Parks	0	0

De-construction

De-construction Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	Total (Since Aug 17)
# of priority sites cleared (out of 10)	2	2.5	0	0	0	1	1	0	1	0	7.5
# Fire Department Connections made accessible	1	2	0	1	0	1	1	9	All Clear	All Clear	15
# of structures taken down	3	3	2	2	2	0	1	0	0	2	15
# new structures have appeared between Abbott and Gore	1	3	1	3	0	0	0	0	0	0	8
# of tents taken down		3	2	1	2	2	3	10	4	2	29
# of carts distributed by Sanitation	15	20	20	14	3	4	0	0	0	0	76
# propane tanks removed	2	2	2	0	0	2	0	3	0	0	11
# flyers distributed	50	0	0	0	0	0	0	0	0	0	50
# of Evelyne Saller meal tickets distributed by ENG teams	25	10	0	0	0	0	45	30	12	20	142
Tonnage of material removed (kg)	2500	4500	3500	3000	2500	3000	2500	2500	2500	2250	n/a
# of Operations Workers deployed	20	18	18	12	12	18	17	17	16	18	n/a
# of Supervisors deployed	3	--	2	1	1	2	2	3	2	3	n/a
# of Managers deployed	1	--	1	1	1	1	1	1	1	1	n/a
# of VFRS Inspectors deployed	4	4	4	2	2	3	4	2	2	0	n/a

Storage & Drop-ins

Storage & Drop-ins Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	Total (Since Aug 17)
# of staffing resources deployed @ Carnegie Outreach	2	2	2	3	3	3	2	0	3	2	n/a
# of totes @ 390 Main (73 tote capacity)	3	4	1	--	0	1	1	10	10	13	n/a
# of people storing totes @ 390 Main (73 tote capacity)	--	3	1	--	0	1	1	8	8	11	n/a
# of totes @ 987 E. Cordova (24 tote capacity)	0	0	0	0	0	0	0	--	0	0	n/a
# of people storing totes @ 987 E. Cordova (24 tote capacity)	--	--	0	0	0	0	0	--	0	0	n/a
# of totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	7	10	--	--	--	10	10	10	10	n/a
# of people storing totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	--	--	--	n/a

Housing & Shelters

Housing & Shelters Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	Total (Since Aug 17)
# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)	0	0	0	2	0	0	0	0	0	1	3
# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)	--	--	--	0	0	0	0	0	0	0	0
# of shelter spaces available today	10	17	14	31	33	35	31	35	41	37	n/a
# of SRO units ready for tenanting today	30	30	30	30	30	30	30	30	50	50	n/a
Estimated # of SRO units available by end of next week	--	--	20	20	20	20	20	20	0	0	n/a

Communications

Communications Metrics	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	Total (Since Aug 2)
# of media requests received and responded to (previous day)	0	0	0	0	1	1	0	5	1		60

* Reporting is 1 day delayed

Monitoring Parks

	New Sheltering In DTES Parks															
	Andy Livingstone Park		Crab Park		Oppenheimer Park		Strathcona Park		McLean Park		Pigeon Park		Other parks		Total	
Date	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People
17-Aug	2	5	7	9	2	2	2	2	0	0	1	2	0	0	14	20
18-Aug	2	--	4	--	3	--	3	--	2	--	1	--	0	0	15	0
19-Aug	1	2	5	5	2	3	1	1	0	0	1	1	0	0	10	12
20-Aug	--	--	--	9	--	5	--	1	--	--	--	--	0	0	0	15
21-Aug	2	3	2	3	2	3	2	2	2	2	1		1	1	12	14
22-Aug	1	2	4	6	2	2	1	2	1	1	1	0	4	5	14	18
23-Aug	4	6	8	10	2	2	1	2	1	1	1	1	2	3	19	25
24-Aug	2	0	5	4	3	7	0	4	1	--	1	2	0	0	12	17
25-Aug	4	6	7	11	2	2	1	1	1	2	1	--	0	0	16	22
26-Aug	4	10	7	9	1	1	0	0	0	0	1				13	20
Total (Since Aug 17)	22	34	49	66	19	27	11	15	8	6	9	6	7	9	147	197

End of document

From: "Zupan, Mike" <mike.zupan@vancouver.ca>
To: "EOC Planning Chief (Vancouver)" s.15(1)(l)
"EOC Situation Report - DL" s.15(1)(l)
Date: 8/27/2022 4:06:58 PM
Subject: Sit Rep - EOC Hastings Destructuring - Aug 27/2022

Hello Everyone,

\~

A brief description of today's Engineering work in the field.

\~

14 people made up our Urban Issues crew along with 1 Supervisor and Manager.\~ The day started with a VPD incident as our team started work on E.Hastings.\~ At approximately 9:30am in front of 57 E. Hastings a member of the public was stabbed in an altercation.\~ COV employees were not involved, however, one employee witnessed part of the event and all Sanitation/Street Ops Employees evacuated and mustered s.15(1)(l) as per our safety protocol. We held an incident debrief and Mental health support was offered and after our discussion all staff felt comfortable to continue work.

\~

The team removed 1 tent, 2 propane tanks, downsized existing structures up and down Hastings with all spaces and doorways that have been previous cleared, remaining open.\~ In addition crews removed 8 unused carts from the street, removed approximately 2000kg of garbage and material and 2 personal possessions carts were moved into storage.\~

\~

The team will be back out on Hastings tomorrow am.

\~

Regards,

\~

Mike

\~

Mike Zupan

Manager, Sanitation Services

Engineering Services | City of Vancouver

Office 604-326-4706

Mobile s.15(1)(l)

\~

\~

\~

From: EOC Planning Chief (Vancouver) s.15(1)(l)
Sent: Friday, August 26, 2022 6:10 PM
To: EOC Situation Report - DL s.15(1)(l)
Subject: Sit Rep - EOC Hastings Destructuring - Aug 26/2022

\~

Hello all,

\~

Please see the attached EOC Situation Report for today, August 26, 2022.

\~

Best,

\~

Gillian Wong

Planning Chief

Emergency Operations Centre

City of Vancouver

E s.15(1)(i)

\~

From: ["EOC Planning Chief \Vancouver\"](#) s.15(1)(l)
To: ["EOC Situation Report - DL"](#) s.15(1)(l)
Date: 9/1/2022 5:57:39 PM
Subject: Sit Rep - EOC Hastings Destructuring - Sept 1/2022
Attachments: 2022-09-01- Situation Report - Hastings Destructuring.pdf

Hello all,

\~

Please see the attached EOC Situation Report for today, Sept 1, 2022.

\~

Best,
Gillian

\~

Gillian Wong | EOC Deputy Planning Chief
City of Vancouver Emergency Operations Centre

s.15(1)(l)

s.15(1)(l)

\~

Situation Report

Event Name	Hastings De-Structuring
Date	Sept 01, 2022
Time	17:45
Operational Period	4 (Sept 01-07)
EOC Activation Level	2
EMBC Task #	N/A
Reviewed By	Gillian Wong, EOC Deputy Planning Chief
Authorized by	Daniel Stevens, EOC Director

This document may be distributed within your municipality or agency
Any distribution outside your agency requires prior approval from the EOC Director

EOC CONTACT INFO

Email: s.15(1)(l)

1. Usual daily EOC meetings were canceled today to provide more time for operations and to allow for meetings to be re-focused
2. Destructuring operations returned to full hours today. Previously cleared areas, doors, and priority sites remain clear.
3. Continue to see an increase of structures in parks outside of the Downtown Eastside.

1. The EOC will be monitoring air quality conditions as fine particulate matter (PM_{2.5}) is increasing in the region. While the outlook for an advisory is high, currently conditions are below an air quality advisory level.
2. Today is the beginning of EOC operational period #4 (Sept 01 - Sept 07). The new EOC Action Plan has been distributed.

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
1	Health and Safety	In progress	<ul style="list-style-type: none"> Safety and training planning and review continued today
2	De-Structuring Operations	In Progress	s.13(1)
	a. Regent Hotel	In Progress	<ul style="list-style-type: none"> All 3 doors and fire connection remains open, working on reducing the material in front of the building.
	b. 7-19 E Hastings	In Progress	<ul style="list-style-type: none"> Ongoing work on reducing the footprint of structures
	c. 41-57 E. Hastings	In Progress	<ul style="list-style-type: none"> Ongoing work on reducing the footprint of structures
	d. 123 & 123 ½ E. Hastings	In Progress	<ul style="list-style-type: none"> Doors remain clear, working on reducing the remaining material in front of the building.
	e. 148-140 E Hastings	In Progress	<ul style="list-style-type: none"> Ongoing work on reducing the footprint of structures
	f. 40-12 E Hastings (market)	In Progress	<ul style="list-style-type: none"> Ongoing work on reducing the footprint of structures
3	Housing and Shelters	Ongoing	s.13(1)

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks

#	Objective	Status/Target	Risks/Issues/Comments
4	Accelerating supports and tactics	NEW	• No update
5	Community Supports		
	a. Outreach Operations	Ongoing	• No update
	b. Comfort stations	Ongoing	• No update
	c. Supports for Indigenous People	Ongoing	• No update
	d. Supports for women	Ongoing	• No update
	e. Storage & Drop in		
	- 320 Alexander (Drop in only)	In progress / Sept 7	• No update
	- 27 W Hastings (Short-term storage; unconfirmed)	NEW	• No update
	- Other storage/drop in spaces (390 Main; 987 E Cordova; 101 E Cordova; 323 Alexander)	Ongoing	• No update

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
	f. Kiosk for Automated Public Toilet (APT) at Pigeon Park	In progress / Sept 9	• No update
	g. Mobile Washroom Trailer - Gore & Hastings	In progress / Sept 16	• No update
6	Communications	In progress / Sept 6	• No update
7	Monitoring Parks	Ongoing/ Issues	s.13(1)
8	Contingency Planning	In progress / Sept 7	• No update

Status Legend:

Not started

In progress

Complete/ Ongoing

On hold/ Issues

Cancelled

Summary: Status & Risks - Continued

#	Objective	Status/Target	Risks/Issues/Comments
9	Interim Sustainment Strategy	In progress/ Sept 7	s.13(1)
10	Coordination with Community Partners	Ongoing	• No issues or risks to report.
11	Track and forecast costs	Ongoing	• No issues or risks to report.
12	EOC Governance & Coordination	NEW	• No update

Status Legend:

Not started

In progress


Complete/ Ongoing

On hold/ Issues

Cancelled

De-construction

80%		% of priority sites cleared (out of 10 sites)
All Clear		# of fire Department Connections made accessible (out of 15)
For Sep 1	Total (Since Aug 17)	
16	68	# of tents and structures taken down
4	16	# of new tents and structures on Hastings (b/w Abbott & Gore)

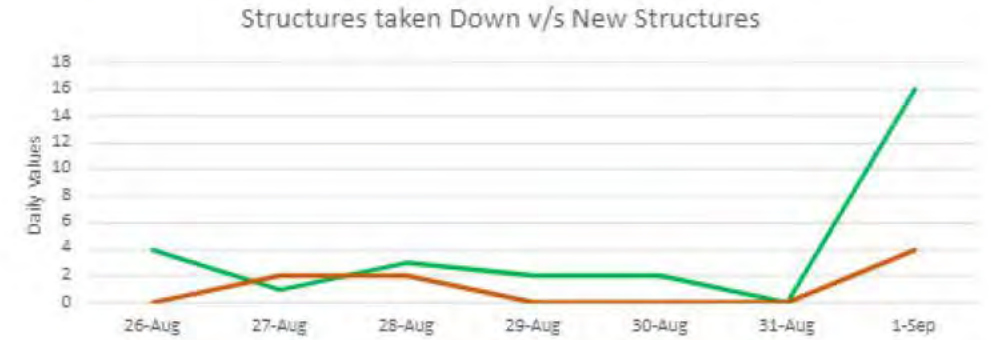

Housing & Shelters

For Sep 1	Total (Since Aug 17)	
2	9	# Unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)
0	0	# Unhoused people within Abbott - Gore that accepted offer of housing (~210 people)
29		# of shelter spaces available today
50		# of SRO units ready for tenanting today
0		Estimated # of SRO units available by end of next week

Communications


For Aug 31 *	Total (Since Aug 2)	
0	63	# of media requests received and responded to (previous day)

* Reporting is 1 day delayed

Monitoring Parks

	Total (Since Aug17)	
	Structures	People
Total New	238	283
	For Sep 1	
	Structures	People
Total New	15	20
Andy Livingstone Park	3	6
Crab Park	7	11
Oppenheimer Park	1	1
Strathcona Park	0	0
McLean Park	1	2
Pigeon Park	1	--
Other Parks	2	--

Cumulative and Daily Metrics Tracking

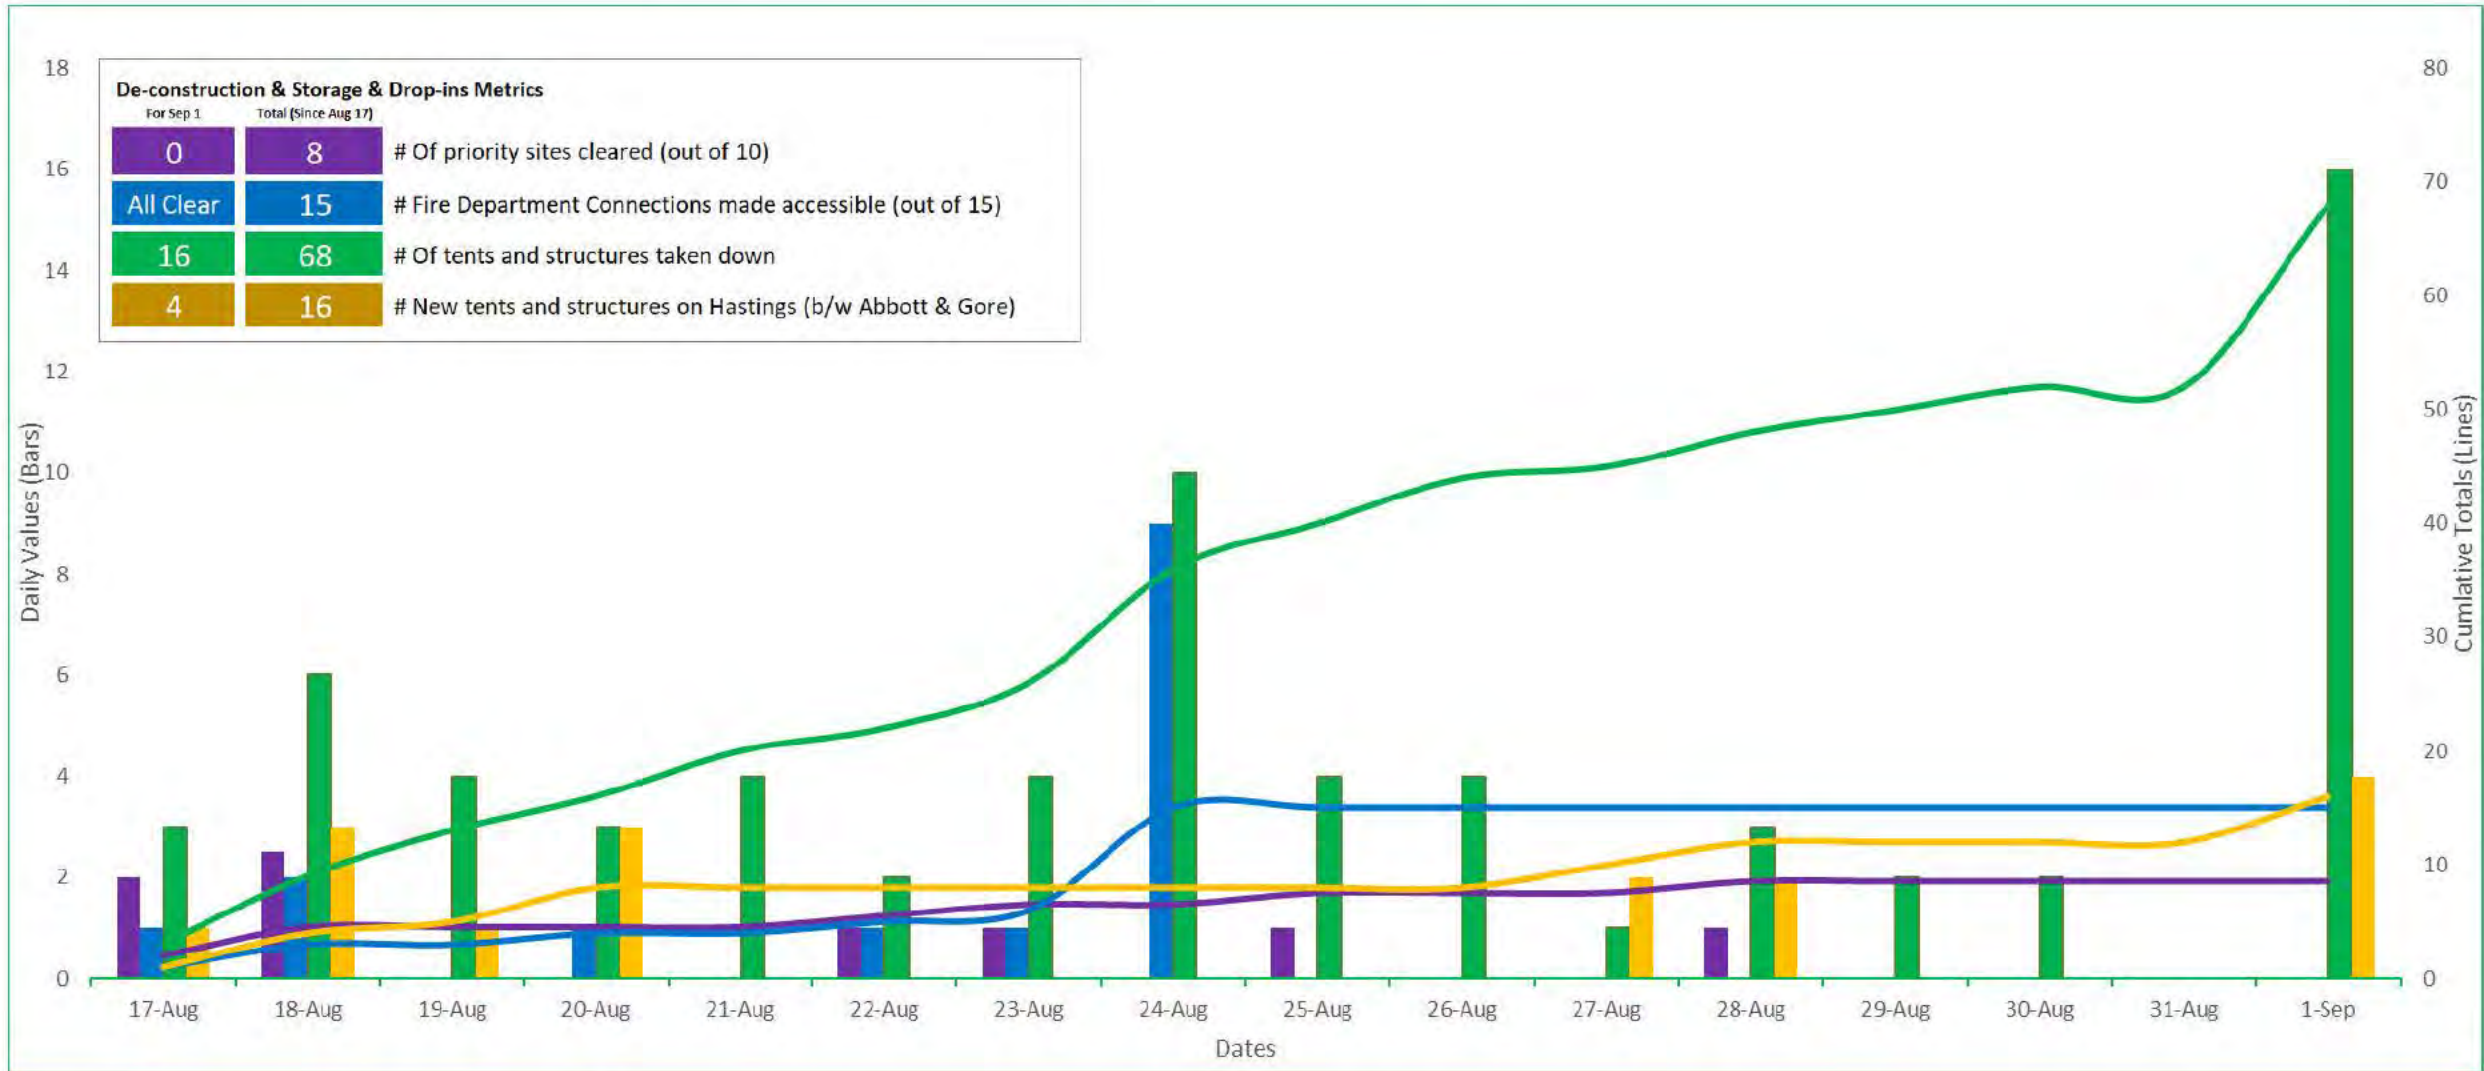

**Note: Operations shortened on Aug 31*

De-construction

De-construction Metrics	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	Total (Since Aug 17)
% of priority sites cleared (out of 10 sites)	0%	70%	80%	80%	80%	80%	80%	n/a
# of fire Department Connections made accessible (out of 15)	All Clear	All Clear	All Clear	All Clear	All Clear	All Clear	All Clear	15
# of tents and structures taken down	4	1	3	2	2	0	16	68
# of new tents and structures on Hastings between Abbott and Gore	0	2	2	0	0	0	4	16
# of carts distributed by Sanitation	0	0	0	2	0	3	0	81
# propane tanks removed	0	2	7	0	0	0	1	21
# flyers distributed	0	0	0	0	0	0	0	50
# of Evelyn Saller meal tickets distributed by ENG teams	20	20	12	20	8	0	20	222
Tonnage of material removed (kg)	2250	2000	2500	2500	2000	1800	2500	n/a
# of Operations Workers deployed	18	14	15	18	15	16	17	n/a
# of Supervisors deployed	3	1	1	1	2	3	2	n/a
# of Managers deployed	1	1	1	1	1	1	1	n/a
# of VFRS Inspectors deployed	0	0	2	0	2	2	2	n/a

Storage & Drop-ins

**Note: Tote metrics will be updated weekly as of Aug 31*

Storage & Drop-ins Metrics	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	Total (Since Aug 17)
# of staffing resources deployed @ Carnegie Outreach	2	3	0	2	4	2	3	n/a
# of totes @ 390 Main (73 tote capacity)	13	--	--	--	--	2	--	22
# of people storing totes @ 390 Main (73 tote capacity)	11	--	--	--	--	1	--	16
# of totes @ 987 E. Cordova (24 tote capacity)	0	--	--	--	--	--	--	n/a
# of people storing totes @ 987 E. Cordova (24 tote capacity)	0	--	--	--	--	--	--	n/a
# of totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	10
# of people storing totes @ 101 E. Cordova - Atira Women's Storage (20 tote capacity)	--	--	--	--	--	--	--	2

Housing & Shelters

Housing & Shelters Metrics	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	Total (Since Aug 17)
# unhoused people within Abbott - Gore that accepted offer of shelter (~210 people)	1	0	0	2	2	0	2	9
# unhoused people within Abbott - Gore that accepted offer of housing (~210 people)	0	0	0	0	0	0	0	0
# of shelter spaces available today	37	35	43	44	28	33	29	n/a
# of SRO units ready for tenanting today	50	50	50	50	50	50	50	n/a
Estimated # of SRO units available by end of next week	0	0	0	0	0	0	0	n/a

Communications

Communications Metrics	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	Total (Since Aug 2)
# of media requests received and responded to (previous day)	1	1	0	0	1	0		63

* Reporting is 1 day delayed

Monitoring Parks

	New Sheltering In DTES Parks															
	Andy Livingstone Park		Crab Park		Oppenheimer Park		Strathcona Park		McLean Park		Pigeon Park		Other parks		Total	
Date	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People	Structures	People
26-Aug	4	10	7	9	1	1	0	0	0	0	1	0	0	0	13	20
27-Aug	6	14	4	0	1	0	0	0	3	3	0	0	4	1	18	18
28-Aug	3	4	6	8	0	0	0	0	1	1	0	0	2	3	12	16
29-Aug	3		5		2	2	1	1	1	1	2		1	2	15	6
30-Aug	5	8	6	6	1	1	0	--	1	2	1	--	2	--	16	17
31-Aug	4	9	8	--	0	0	1	--	1	--	1	--	--	--	15	9
1-Sep	3	6	7	11	1	1	0	0	1	2	1	--	2	--	15	20
Total (Since Aug 17)	46	75	85	91	24	31	13	16	16	15	14	6	18	15	238	283

End of document

From: "Hesse, Bradley" <Bradley.Hesse@vancouver.ca>
To: "VFRS Duty Chiefs - DL" s.15(1)(l)
Date: 8/8/2022 11:48:43 PM
Subject: Structure Fire 403 E Hastings

E1, L1, E2, L2, E8, L8, L3, R2, B1, AC01 to 403 E Hastings for single caller report of fire in the building.
E2 first on scene, found fire in suite 502 out on arrival by sprinklers.

Patricia Hotel, 6 story building.

No extension.

Alarm bells ringing.

Initial report of possible lithium battery fire.

No report of injuries.

B1 requested Fire Investigator, and began to release apparatus.

VPD and EHS on scene.

FI is investigating, E2 will be staying on scene with FI.

Management will be taking care of any displaced tenants.

/~
/~
/~
/~



Brad Hesse (he/him/his)

Assistant Chief Operations C Shift, Vancouver Fire & Rescue Services

City of Vancouver | 900 Heatley Avenue | Vancouver BC V6A 3S7

t: (604) 665-6040

c: s.15(1)(l)

e: Bradley.Hesse@Vancouver.ca

/~
/~

From: ["Bertuzzi, Brian" <Brian.Bertuzzi@vancouver.ca>](mailto:Brian.Bertuzzi@vancouver.ca)
To: ["VFRS Duty Chiefs - DL"](#) s.15(1)(l)
Date: 9/1/2022 5:22:20 AM
Subject: Tents/waste fire, E. Hastings

ST5 assignment responded to 438 E Hastings. Fire knocked down quickly by 2 Company. No injuries reported, no structures appear damaged. FI en route.



Sent from my iPhone

From: ["Myles, Miranda" <Miranda.Myles@vancouver.ca>](mailto:Miranda.Myles@vancouver.ca)
To: ["Mochrie, Paul" <Paul.Mochrie@vancouver.ca>](mailto:Paul.Mochrie@vancouver.ca)
["Rosa, Donnie" <Donnie.Rosa@vancouver.ca>](mailto:Donnie.Rosa@vancouver.ca)
["Jasper, Kirsten" <Kirsten.Jasper@vancouver.ca>](mailto:Kirsten.Jasper@vancouver.ca)
["Melles, Bruk" <Bruk.Melles@vancouver.ca>](mailto:Bruk.Melles@vancouver.ca)
["Lam, Phoenix" <Phoenix.Lam@vancouver.ca>](mailto:Phoenix.Lam@vancouver.ca)
["Ali, Shabna" <Shabna.Ali@vancouver.ca>](mailto:Shabna.Ali@vancouver.ca)
["Vajanto, Laura" <Laura.Vajanto@vancouver.ca>](mailto:Laura.Vajanto@vancouver.ca)
["Kapoor, Sarah" <Sarah.Kapoor@vancouver.ca>](mailto:Sarah.Kapoor@vancouver.ca)
["Ralph, Alexander" <Alexander.Ralph@vancouver.ca>](mailto:Alexander.Ralph@vancouver.ca)
["EOC Planning Chief \\\\(Vancouver\\)" s.15\(1\)\(f\)](#)
["Wong, Gillian" <Gillian.Wong@vancouver.ca>](mailto:Gillian.Wong@vancouver.ca)
["Clark, Elizabeth" <Elizabeth.Clark@vancouver.ca>](mailto:Elizabeth.Clark@vancouver.ca)
["Mital, Eric" <Eric.Mital@vancouver.ca>](mailto:Eric.Mital@vancouver.ca)
["Beatch, Laurence" <Laurence.Beatch@vancouver.ca>](mailto:Laurence.Beatch@vancouver.ca)
["Davidson, Catherine" <Catherine.Davidson@vancouver.ca>](mailto:Catherine.Davidson@vancouver.ca)
["Wilson, Darcy" <Darcy.Wilson@vancouver.ca>](mailto:Darcy.Wilson@vancouver.ca)
["Savage, Gordon" <Gordon.Savage@vancouver.ca>](mailto:Gordon.Savage@vancouver.ca)
["Hurford, Dianna" <Dianna.Hurford@vancouver.ca>](mailto:Dianna.Hurford@vancouver.ca)
["Tardif-Bennett, Ashley" <Ashley.Tardif-Bennett@vancouver.ca>](mailto:Ashley.Tardif-Bennett@vancouver.ca)
["Walker, Breanna" <Breanna.Walker@vancouver.ca>](mailto:Breanna.Walker@vancouver.ca)
["Chami, Beata" <Beata.Chami2@vancouver.ca>](mailto:Beata.Chami2@vancouver.ca)
["Rana, Preet" <Preet.Rana@vancouver.ca>](mailto:Preet.Rana@vancouver.ca)
["McDonald, Gordon" <Gordon.McDonald@vancouver.ca>](mailto:Gordon.McDonald@vancouver.ca)
Caitlin.Etherington@vch.ca
Elizabeth.Holliday@vch.ca
adunnet@bchousing.org
["Stevens, Daniel" <Daniel.Stevens@vancouver.ca>](mailto:Daniel.Stevens@vancouver.ca)
["Levitt, Karen" <karen.levitt@vancouver.ca>](mailto:karen.levitt@vancouver.ca)
["Singh, Sandra" <Sandra.Singh@vancouver.ca>](mailto:Sandra.Singh@vancouver.ca)
["LaClaire, Lon" <lon.laclair@vancouver.ca>](mailto:lon.laclair@vancouver.ca)
["CHOW, Howard \\\\(VPD\\)" <howard.chow@vpd.ca>](mailto:howard.chow@vpd.ca)
["Fry, Karen" <Karen.Fry@vancouver.ca>](mailto:Karen.Fry@vancouver.ca)
["Impey, Patrice" <Patrice.Impey@vancouver.ca>](mailto:Patrice.Impey@vancouver.ca)
["Henselmann, Branislav" <Branislav.Henselmann@vancouver.ca>](mailto:Branislav.Henselmann@vancouver.ca)
["Zak, MaryClare" <MaryClare.Zak@vancouver.ca>](mailto:MaryClare.Zak@vancouver.ca)
["Baker, Sue" <Sue.Baker@vancouver.ca>](mailto:Sue.Baker@vancouver.ca)
["Zupan, Mike" <mike.zupan@vancouver.ca>](mailto:mike.zupan@vancouver.ca)
["Hogan, Paul \\\\(eng\\)" <Paul.Hogan@vancouver.ca>](mailto:Paul.Hogan@vancouver.ca)
["Sidwell, Amy" <Amy.Sidwell@vancouver.ca>](mailto:Amy.Sidwell@vancouver.ca)
["Scollard, Taryn" <taryn.scollard@vancouver.ca>](mailto:taryn.scollard@vancouver.ca)

[<Betty.Lepps@vancouver.ca>](mailto:Betty.Lepps@vancouver.ca)
[<Amit.Gandha@vancouver.ca>](mailto:Amit.Gandha@vancouver.ca)
[<don.chapman@vpd.ca>](mailto:don.chapman@vpd.ca)
[<shaun.deans@vpd.ca>](mailto:shaun.deans@vpd.ca)
[<dave.meers@vancouver.ca>](mailto:dave.meers@vancouver.ca)
[<tyler.moore@vancouver.ca>](mailto:tyler.moore@vancouver.ca)
[<Angela.MacKenzie@vancouver.ca>](mailto:Angela.MacKenzie@vancouver.ca)
[<Godfrey.Tait@vancouver.ca>](mailto:Godfrey.Tait@vancouver.ca)
[<Darryl.Lagerquist@vancouver.ca>](mailto:Darryl.Lagerquist@vancouver.ca)
[<Armin.Amrolia@vancouver.ca>](mailto:Armin.Amrolia@vancouver.ca)
[<Jason.Mah@vancouver.ca>](mailto:Jason.Mah@vancouver.ca)
[<Maria.Pontikis@vancouver.ca>](mailto:Maria.Pontikis@vancouver.ca)
[<celine.mauboules@vancouver.ca>](mailto:celine.mauboules@vancouver.ca)

Date: 8/26/2022 5:31:04 PM

Subject: Update: Hastings Leadership Group Weekend Meetings

Hi All,

As discussed on the call today we will be cancelling the invite to the 3pm meetings on Saturday and Sunday and a separate invite will be sent to those who are working over the weekend.\~ The new 3pm invite will come out tomorrow morning for an end of day check in meeting for the smaller group.\~

\~

Thank you,
Miranda

\~

-----Original Appointment-----

From: Vodounou, Irene On Behalf Of Stevens, Daniel

Sent: Thursday, August 25, 2022 1:02 PM

To: Stevens, Daniel; Levitt, Karen; Singh, Sandra; LaClaire, Lon; CHOW, Howard (VPD); Fry, Karen; Impey, Patrice; Henselmann, Branislav; Zak, MaryClare; Baker, Sue; Zupan, Mike; Hogan, Paul (eng); Sidwell, Amy; Scollard, Taryn; Lepps, Betty; Gandha, Amit; CHAPMAN, Don; DEANS, Shaun; Meers, Dave; Moore, Tyler; MacKenzie, Angela; Tait, Godfrey; Lagerquist, Darryl; Amrolia, Armin; Mah, Jason; Pontikis, Maria; Mauboules, Celine

Cc: Mochrie, Paul; Rosa, Donnie; Jasper, Kirsten; Melles, Bruk; Lam, Phoenix; Ali, Shabna; Vajanto, Laura; Kapoor, Sarah; Ralph, Alexander; EOC Planning Chief (Vancouver); Wong, Gillian; Clark, Elizabeth; Mital, Eric; Beatch, Laurence; Davidson, Catherine; Wilson, Darcy; Savage, Gordon; Hurford, Dianna; Tardif-Bennett, Ashley; Myles, Miranda; Walker, Breanna; Chami, Beata; Rana, Preet; McDonald, Gordon; 'Caitlin.Etherington@vch.ca'; 'Elizabeth.Holliday@vch.ca'; 'adunnet@bchousing.org'

Subject: Hastings Leadership Group

When: Saturday, August 27, 2022 3:00 PM-3:30 PM (UTC-08:00) Pacific Time (US & Canada).

Where: Microsoft Teams Meeting

\~

Purpose: \~daily check-in call regarding Hastings Street for the next two weeks.
Staff on vacation are not expected to dial-in.

\~

This meeting invite replaces the 5pm meeting series with the same name from Paul Mochrie.

\~

Given feedback from the group, this meeting invitation may be adjusted to 4:30pm in the future.

\~

Thank you!

Daniel

\~

Microsoft Teams meeting

Join on your computer or mobile app

[Click here to join the meeting](#)

Meeting ID: s.15(1)(l)

Passcode: s.15(1)(l)

[Download Teams](#) | [Join on the web](#)

Or call in (audio only)

+1 604-665-6000, s.15(1)(l)

Phone Conference ID: s.15(1)(l)

[Find a local number](#) | [Reset PIN](#)

Personal Information collected via MS365 Teams Mtgs will be used by the City of Vancouver for managing mtg attendance and collaboration under the authority of s.26(c) of FIPPA. Questions may be emailed to the Director, ATIP, privacy@vancouver.ca

[Learn More](#) | [Meeting options](#)

\~

From: "Melles, Bruk" <Bruk.Melles@vancouver.ca>
To: "Scollard, Taryn" <taryn.scollard@vancouver.ca>
"Renning, Rob" <rob.renning@vancouver.ca>
"Meers, Dave" <dave.meers@vancouver.ca>
"Tran, Tan" <tan.tran@vpd.ca>
"Henselmann, Branislav" <Branislav.Henselmann@vancouver.ca>
"Zak, MaryClare" <MaryClare.Zak@vancouver.ca>
"Zupan, Mike" <mike.zupan@vancouver.ca>
"Mauboules, Celine" <celine.mauboules@vancouver.ca>
"Domes, Krystyna" <Krystyna.Domes@vancouver.ca>
"Lam, Phoenix" <Phoenix.Lam@vancouver.ca>
"Shamess, Albert" <Albert.Shamess@vancouver.ca>
"Fry, Karen" <Karen.Fry@vancouver.ca>
"Parker, Lisa" <Lisa.Parker@vancouver.ca>
"Lepps, Betty" <Betty.Lepps@vancouver.ca>
"Sidwell, Amy" <Amy.Sidwell@vancouver.ca>
"Rosa, Donnie" <Donnie.Rosa@vancouver.ca>
"Guerette, Jeannine" <Jeannine.Guerette@vancouver.ca>
"LaClaire, Lon" <lon.laclaire@vancouver.ca>
"Baker, Sue" <Sue.Baker@vancouver.ca>
"McElroy, Jeremy" <Jeremy.McElroy@vancouver.ca>
"Singh, Sandra" <Sandra.Singh@vancouver.ca>

Date: 8/8/2022 5:06:38 PM

Subject: Updated Hastings Ops Plan - August 8,2022

Attachments: ACCS - HHS - Hastings Deconstructing Operational Plan - July 2022 - DRAFT.tr5

Hi Everyone,

\~

Please find attached the latest draft of the Hastings Operations Plan. This continues to be a living document, updated as the situation evolves.\~

We had a classic Vandocs scare about an hour ago (known problem, version 10 issue!)

\~

Please add any edit suggestions using "comments" in track changes. **Please do not edit the actual content.**

\~

This document remains confidential and not for distribution at this point.

\~

\~

Respectfully,

Bruk

\~

\~

\~

Brak Melles | Director, Homelessness Services

Housing & Homelessness Services

Arts, Culture & Community Services | City of Vancouver

bruk.melles@vancouver.ca

Mobile: s.15(1)(l)

Pronouns: \~ she/her/hers

\~

I am humbly thankful that I live and work on the unceded homelands of the xʷməθNə́m̓ (Musqueam),

Skwámú 7mesh (Squamish), and səlilwətał (Tsleil-Waututh) Peoples

\~

